6000 0748

Mining District File Summary Sheet

DISTRICT	Rosebud
DIST_NO	4010
COUNTY If different from written on document	Pershing
TITLE If not obvious	Rosebud Drill Hole File - Hole No. RBW-15
AUTHOR	R. Vance; B. Werner
DATE OF DOC(S)	1995, 1998
MULTI_DIST Y / N? Additional Dist_Nos:	
QUAD_NAME	Sulphur 7.5'
P_M_C_NAME (mine, claim & company names)	Rosebud Mine; Hecla Mining Co Hecla Rosebud Mine
COMMODITY If not obvious	gold; silver
NOTES	drill logs; geology; assay; total depth 1330' water; hand written notes; pump information 15 p

Keep docs at about 250 pages if no oversized maps attached
(for every 1 oversized page (>11x17) with text reduce
the amount of pages by ~25)

SS: DJ 4/30/08
Initials Date
DB:
Initials Date
SCANNED:
Initials Date

Revised: 1/22/08

RBW - 15

6000 0748
4010

60000748

RBW-15

WHITE—DIVISION OF WATER RESOURCES
CANARY—CLIENT'S COPY
PINK—WELL DRILLER'S COPY

PRINT OR TYPE ONLY
DO NOT WRITE ON BACK

STATE OF NEVADA
DIVISION OF WATER RESOURCES

WELL DRILLER'S REPORT

Please complete this form in its entirety in accordance with NRS 534.170 and NAC 534.340

OFFICE USE ONLY
Log No.
Permit No.
Basin

NOTICE OF INTENT NO. 29508

1. OWNER HECLA MINING COMPANY
MAILING ADDRESS 6500 MINERAL DR.
COEUR D'ALENE, ID 83814-8788

ADDRESS AT WELL LOCATION
HECLA ROSEBUD MINE

2. LOCATION NW ¼ NW ¼ Sec. 19 T. 34 ☐ N/S R. 30 E. PERSHING County

PERMIT NO. N/A (Issued by Water Resources) | N/A (Parcel No.) | N/A (Subdivision Name)

3. WORK PERFORMED
☒ New Well ☐ Replace ☐ Recondition
☐ Deepen ☐ Abandon ☐ Other

4. PROPOSED USE
☐ Domestic ☐ Irrigation ☐ Test
☒ Municipal/Industrial ☐ Monitor ☐ Stock

5. WELL TYPE
☐ Cable ☐ Rotary ☒ RVC
☐ Air ☐ Other

6. LITHOLOGIC LOG

Material	Water Strata	From	To	Thickness
VOLCANICS		0	1166	1166
SEDIMENTARY		1166	1330	164

8" CASING CEMENTED FROM
1050' TO 925'
FOR POSSIBLE FRACTURING

Date started NOVEMBER 26, 19 95
Date completed DECEMBER 6, 19 95

7. WELL TEST DATA

TEST METHOD: ☐ Bailer ☐ Pump ☒ Air Lift

G.P.M.	Draw Down (Feet Below Static)	Time (Hours)
100	80	2

8. WELL CONSTRUCTION
Depth Drilled 1330 Feet Depth Cased 1320 Feet

HOLE DIAMETER (BIT SIZE)

		From	To
20-1/2 Inches		0 Feet	19 Feet
14-3/4 Inches		19 Feet	1330 Feet
Inches		Feet	Feet

CASING SCHEDULE

Size O.D. (Inches)	Weight/Ft. (Pounds)	Wall Thickness (Inches)	From (Feet)	To (Feet)
16	62.58	.375	0	19
8-5/8	28.55	.322	+2	1320

Perforations:
Type perforation SLOTTED & LOUVERED
Size perforation .100
From 1160 feet to 1220 feet LOUVE
From 1220 feet to 1300 feet SLOTT
From feet to feet
From feet to feet
From feet to feet

Surface Seal: ☒ Yes ☐ No
Depth of Seal 50
Placement Method: ☒ Pumped ☐ Poured

Seal Type: ☒ Neat Cement ☐ Cement Grout ☐ Concrete Grout

Gravel Packed: ☒ Yes ☐ No
From 50 feet to 1330 feet

9. WATER LEVEL
Static water level 600 feet below land surface
Artesian flow G.P.M. P.S.I.
Water temperature °F Quality GOOD

10. DRILLER'S CERTIFICATION
This well was drilled under my supervision and the report is true to the best of my knowledge.
Name LANG EXPLORATORY DRILLING (Contractor)
Address 2286 WEST 1500 SOUTH (Contractor)
SALT LAKE CITY, UTAH 84104
Nevada contractor's license number issued by the State Contractor's Board 0021976
Nevada driller's license number issued by the Division of Water Resources, the on-site driller 1733
Signed BRYON WERNER Bryon Werner
By driller performing actual drilling on site or contractor
Date 12-07-95

(Rev. 3-91) USE ADDITIONAL SHEETS IF NECESSARY (O)-627

SPO 36052.123 12/95

From: AAL Assay Report

11/4/98

R. B. Vance

			Au	Au(R)	Ag
			ppb	ppb	ppm
			FA60	FA60	D210
RBW-15	0	10	17	0	0.6
RBW-15	10	20	8	0	<0.5
RBW-15	20	30	<5	0	<0.5
RBW-15	30	40	<5	0	<0.5
RBW-15	40	50	<5	0	0.5
RBW-15	50	60	<5	0	<0.5
RBW-15	60	70	<5	0	<0.5
RBW-15	70	80	189	0	3.8
RBW-15	80	90	198	0	4.7
RBW-15	90	100	235	0	2.8
RBW-15	100	110	14	0	3
RBW-15	110	120	92	0	1.7
RBW-15	120	130	<5	<5	0.5
RBW-15	130	140	<5	0	<0.5
RBW-15	140	150	21	0	0.6
RBW-15	150	160	11	0	0.8
RBW-15	160	170	<5	0	<0.5
RBW-15	170	180	<5	0	<0.5
RBW-15	180	190	92	0	1.2
RBW-15	190	200	263	0	2.4
RBW-15	200	210	275	0	4
RBW-15	210	220	52	0	2.1
RBW-15	220	230	26	0	1.1
RBW-15	230	240	14	0	1
RBW-15	240	250	12	0	0.5
RBW-15	250	260	<5	0	<0.5
RBW-15	260	270	<5	0	<0.5
RBW-15	270	280	<5	0	<0.5
RBW-15	280	290	24	0	1.3
RBW-15	290	300	18	0	1.1
RBW-15	300	310	<5	0	0.5
RBW-15	310	320	<5	0	<0.5
RBW-15	320	330	<5	0	0.7
RBW-15	330	340	<5	0	<0.5
RBW-15	340	350	13	0	1.2
RBW-15	350	360	<5	0	0.8
RBW-15	360	370	<5	0	<0.5
RBW-15	370	380	<5	0	<0.5
RBW-15	380	390	<5	0	<0.5
RBW-15	390	400	<5	0	<0.5
RBW-15	400	410	<5	0	<0.5
RBW-15	410	420	<5	0	<0.5
RBW-15	420	430	<5	0	<0.5
RBW-15	430	440	<5	0	<0.5
RBW-15	440	450	<5	0	<0.5
RBW-15	450	460	<5	0	<0.5
RBW-15	460	470	<5	0	<0.5
RBW-15	470	480	<5	0	<0.5
RBW-15	480	490	<5	0	<0.5
RBW-15	490	500	<5	<5	<0.5
RBW-15	500	510	<5	0	<0.5
RBW-15	510	520	<5	0	<0.5
RBW-15	520	530	<5	0	<0.5

RBW-15 PUMP & MOTOR

2286 W. 1500 S.
SLC, UTAH 84104

WELL 1330' DEEP (LANG EXPLORATION)
WATER @ ≈ 600' DEEP (STATIC WATER LEVEL)
CASED TO 1320' (8 5/8" O.D.)
LOUVER 1160' TO 1220'
SLOTTED 1220' TO 1300'
GRAVEL PACKED 50' TO 1330'
NEAT CEMENT PUMPED SURFACE TO 50'
AIR LIFT (WELL TEST DATA)
100 GPM DRAWN DOWN (FEET BELOW STATIC) 80'
2 HOURS
11-26-95 TO 12-6-95

PUMP CROWN MODEL 56-230-15A
SET @ 1128' - 6"
MOTOR FRANKLIN SUBMERSIBLE MOTOR

FALLON

PARSONS DRILLING INSTALLED?

CROWN

S6-230

MODEL S6-230-15A
PERFORMANCE CHARACTERISTICS

MINIMUM WELL SIZE 6"

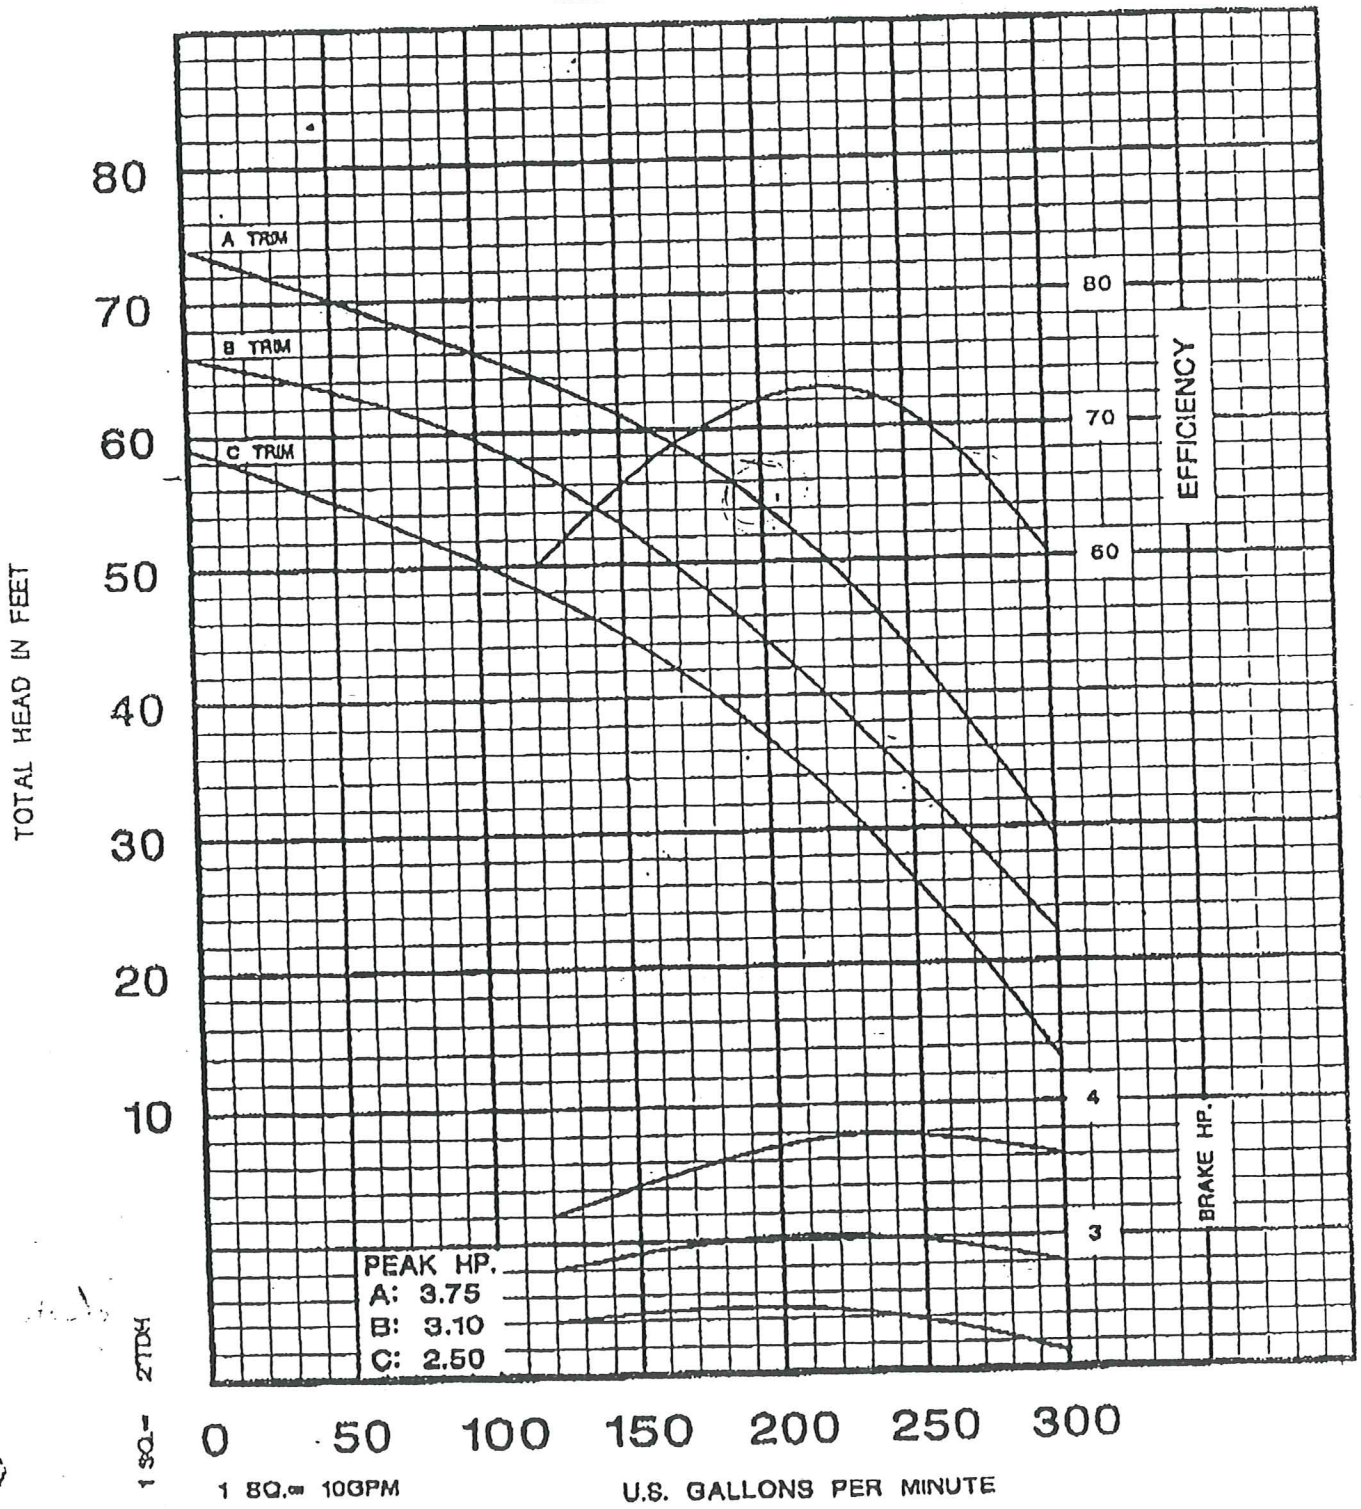

CROWN CROWN PUMP CORPORATION , HIGHWAY 16 & BIVAR , DE LEON , TEXAS

MODEL S6-230

GENERAL DATA

RPM: 3500 NOMINAL, 60HZ.
MAX. O.D. W/CABLE GUARD 5 7/8"
MINIMUM WELL SIZE 6"
DISCHARGE SIZE: 4" STANDARD

BOWLS : CAST IRON
IMPELLERS : BRONZE
SHAFT : STAINLESS STEEL

IMPELLER DATA

IMPELLER NO.: 613
TYPE : ENCLOSED
EFFECTIVE EYE AREA : 5.3 SQ. IN.
TRIM DIAMETER
A - 4.800"
B - 4.500"
C - 4.300"
D -
E -

THRUST CONSTANT K: 2.8
NO. OF VANES : 6
IMPELLER SKIRT CLEARANCE : .015"
EFFICIENCY CORRECTION
1 STAGE - 3%
2 STAGE - 2%
3 STAGE - 1%
4 STAGE - 0

BOWL DATA

BOWL NO. : 561
DIAMETER : 5.5"
CONNECTION : THREADED

SHAFT BEARING CLEARANCE : .010"
BEARING MATERIAL: CUTLESS RUBBER
PUMP SHAFT DIAMETER : 1"

SPECIAL MATERIALS AVAILABLE - CONTACT FACTORY

NOTE: EFFICIENCY PERFORMANCE BASED ON CAST IRON BOWLS - POLISHED BRONZE IMPELLERS AND 6 FEET SUBMERGENCE.

THIS CHARACTERISTIC CURVE IS BASED ON FACTORY TESTS WHEN PUMPING CLEAR, NONAERATED WATER AT A TEMPERATURE NOT EXCEEDING 85 F. AND UNDER SUCTION CONDITIONS AS INDICATED. SPECIFICATIONS SUBJECT TO CHANGE WITHOUT NOTICE.
PUMP PERFORMANCE RATING IS FOR THE DESIGNATED POINT ONLY AND IS SUBJECT TO TEST TOLERANCES AND PROCEDURES AS SPECIFIED IN THE STANDARD OF THE HYDRAULIC INSTITUTE.

WEIGHT

1 STAGE PUMP : 64#
ADD. STAGE : 15#

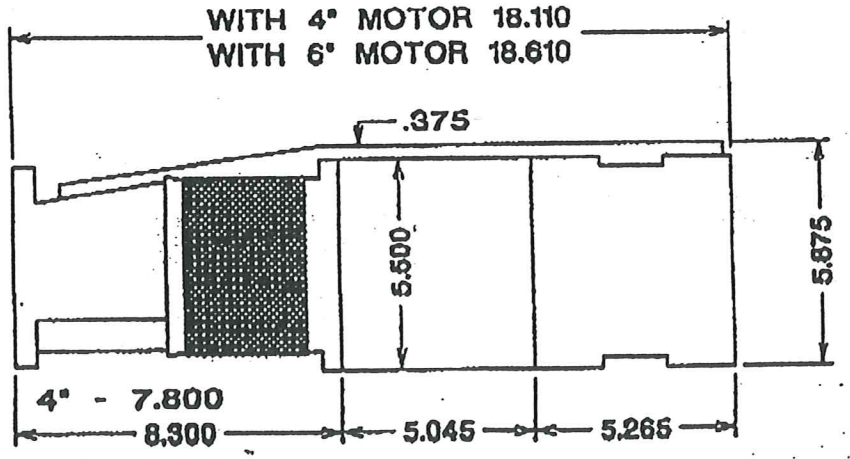

DISCHARGES AVAILABLE
3" FEMALE
4" MALE
4" FEMALE

CROWN CROWN PUMP CORPORATION , HIGHWAY 16 & BIVAR , DE LEON , TEXAS

From: AAL Assay Report
11/4/98
R. B. Vance

			Au	Au(R)	Ag
			ppb	ppb	ppm
			FA60	FA60	D210
RBW-15	0	10	17	0	0.6
RBW-15	10	20	8	0	<0.5
RBW-15	20	30	<5	0	<0.5
RBW-15	30	40	<5	0	<0.5
RBW-15	40	50	<5	0	0.5
RBW-15	50	60	<5	0	<0.5
RBW-15	60	70	<5	0	<0.5
RBW-15	70	80	189	0	3.8
RBW-15	80	90	198	0	4.7
RBW-15	90	100	235	0	2.8
RBW-15	100	110	14	0	3
RBW-15	110	120	92	0	1.7
RBW-15	120	130	<5	<5	0.5
RBW-15	130	140	<5	0	<0.5
RBW-15	140	150	21	0	0.6
RBW-15	150	160	11	0	0.8
RBW-15	160	170	<5	0	<0.5
RBW-15	170	180	<5	0	<0.5
RBW-15	180	190	92	0	1.2
RBW-15	190	200	263	0	2.4
RBW-15	200	210	275	0	4
RBW-15	210	220	52	0	2.1
RBW-15	220	230	26	0	1.1
RBW-15	230	240	14	0	1
RBW-15	240	250	12	0	0.5
RBW-15	250	260	<5	0	<0.5
RBW-15	260	270	<5	0	<0.5
RBW-15	270	280	<5	0	<0.5
RBW-15	280	290	24	0	1.3
RBW-15	290	300	18	0	1.1
RBW-15	300	310	<5	0	0.5
RBW-15	310	320	<5	0	<0.5
RBW-15	320	330	<5	0	0.7
RBW-15	330	340	<5	0	<0.5
RBW-15	340	350	13	0	1.2
RBW-15	350	360	<5	0	0.8
RBW-15	360	370	<5	0	<0.5
RBW-15	370	380	<5	0	<0.5
RBW-15	380	390	<5	0	<0.5
RBW-15	390	400	<5	0	<0.5
RBW-15	400	410	<5	0	<0.5
RBW-15	410	420	<5	0	<0.5
RBW-15	420	430	<5	0	<0.5
RBW-15	430	440	<5	0	<0.5
RBW-15	440	450	<5	0	<0.5
RBW-15	450	460	<5	0	<0.5
RBW-15	460	470	<5	0	<0.5
RBW-15	470	480	<5	0	<0.5
RBW-15	480	490	<5	0	<0.5
RBW-15	490	500	<5	<5	<0.5
RBW-15	500	510	<5	0	<0.5
RBW-15	510	520	<5	0	<0.5
RBW-15	520	530	<5	0	<0.5

RBW-15	530	540	<5	0	<0.5
RBW-15	540	550	<5	0	<0.5
RBW-15	550	560	<5	0	<0.5
RBW-15	560	570	<5	0	<0.5
RBW-15	570	580	<5	0	<0.5
RBW-15	580	590	<5	0	<0.5
RBW-15	590	600	<5	0	<0.5
RBW-15	600	610	<5	0	<0.5
RBW-15	610	620	<5	0	<0.5
RBW-15	620	630	<5	0	<0.5
RBW-15	630	640	<5	0	<0.5
RBW-15	640	650	<5	0	<0.5
RBW-15	650	660	<5	<5	<0.5
RBW-15	660	670	<5	0	<0.5
RBW-15	670	680	<5	0	<0.5
RBW-15	680	690	<5	0	<0.5
RBW-15	690	700	<5	0	0.5
RBW-15	700	710	<5	0	<0.5
RBW-15	710	720	<5	<5	<0.5
RBW-15	720	730	<5	0	<0.5
RBW-15	730	740	32	0	1.2
RBW-15	740	750	16	0	0.8
RBW-15	750	760	<5	0	0.6
RBW-15	760	770	26	0	0.8
RBW-15	770	780	20	0	0.7
RBW-15	780	790	20	0	0.7
RBW-15	790	800	15	0	0.7
RBW-15	800	810	34	28	0.9
RBW-15	810	820	23	0	0.7
RBW-15	820	830	<5	0	1.2
RBW-15	830	840	20	0	0.5
RBW-15	840	850	10	0	<0.5
RBW-15	850	860	16	0	<0.5
RBW-15	860	870	28	0	1
RBW-15	870	880	40	0	0.7
RBW-15	880	890	40	0	0.7
RBW-15	890	900	41	0	0.5
RBW-15	900	910	34	0	0.6
RBW-15	910	920	34	0	0.6
RBW-15	920	930	27	0	0.6
RBW-15	930	940	19	0	<0.5
RBW-15	940	950	8	5	<0.5
RBW-15	950	960	10	0	<0.5
RBW-15	960	970	20	0	<0.5
RBW-15	970	980	111	0	1
RBW-15	980	990	<5	0	<0.5
RBW-15	990	1000	<5	0	<0.5
RBW-15	1000	1010	8	0	<0.5
RBW-15	1010	1020	<5	<5	<0.5
RBW-15	1020	1030	<5	0	<0.5
RBW-15	1030	1040	<5	0	<0.5
RBW-15	1040	1050	81	0	<0.5
RBW-15	1050	1060	48	0	<0.5
RBW-15	1060	1070	<5	0	<0.5
RBW-15	1070	1080	9	0	<0.5
RBW-15	1080	1090	52	0	0.5

RBW-15	1090	1100	8	0	<0.5
RBW-15	1100	1110	<5	0	<0.5
RBW-15	1110	1120	5	0	<0.5
RBW-15	1120	1130	<5	0	<0.5
RBW-15	1130	1140	<5	0	<0.5
RBW-15	1140	1150	<5	<5	<0.5
RBW-15	1150	1160	<5	0	<0.5
RBW-15	1160	1170	22	0	1.3
RBW-15	1170	1180	47	0	1.6
RBW-15	1180	1190	45	0	1.3
RBW-15	1190	1200	9	0	1
RBW-15	1200	1210	5	0	1.1
RBW-15	1210	1220	17	0	0.9
RBW-15	1220	1230	9	0	<0.5
RBW-15	1230	1240	11	12	0.5
RBW-15	1240	1250	168	0	1.5
RBW-15	1250	1260	<5	0	0.5
RBW-15	1260	1270	19	0	0.8
RBW-15	1270	1280	<5	0	0.7
RBW-15	1280	1290	29	0	1
RBW-15	1290	1300	60	0	0.6
RBW-15	1300	1310	9	0	0.8
RBW-15	1310	1320	<5	0	0.7
RBW-15	1320	1330	5	0	0.6
RBW-15	1330	1340	<5	0	0.5
RBW-15	1340	1350	<5	0	0.7
RBW-15	1350	1360	<5	0	0.5
RBW-15	1360	1370	112	132	1.1
RBW-15	1370	1380	<5	<5	0.5
RBW-15	1380	1390	7	0	0.8
RBW-15	1390	1400	14	0	1.1

AMERICAN ASSAY LABORATORIES

PROVISIONAL REPORT SP036052

P.O. BOX 11530
RENO. NV,,USA
Ph.1-702-356-0606, Fax.1-702-356-1413

HECLA MINING CO.

COPIES TO : CHARLIE MUERHOFF

:

:

:

CLIENT REFERENCE No: RBW-15 RECEIVED : 18 OCT 1995

No. SAMPLES : 140 REPORTED : 6 NOV 1995

MAIN SAMPLE TYPE : DRILL CUTTINGS

ANALYSIS	ANALYTICAL METHOD	QUALITY PARAMETER	UNIT	DETECTION
Au	FA60	15%	ppb	5
Au(R)	FA60	15%	ppb	5
Ag	D210	10%	ppm	0.5

SIGNATORY : Sue King N.S.

AMERICAN ASSAY LABORATORIES

PROVISIONAL REPORT SP036052

CLIENT : HECLA MINING CO.
PROJECT : ROSEBUD
REFERENCE : RBW-15

REPORTED : 6 NOV 1995

SAMPLES	Au	Au(R)	Ag
RBW-15 0000-0010	17		0.6
RBW-15 0010-0020	8		<0.5
RBW-15 0020-0030	<5		<0.5
RBW-15 0030-0040	<5		<0.5
RBW-15 0040-0050	<5		0.5
RBW-15 0050-0060	<5		<0.5
RBW-15 0060-0070	<5		<0.5
RBW-15 0070-0080	189		3.8
RBW-15 0080-0090	198		4.7
RBW-15 0090-0100	235		2.8
RBW-15 0100-0110	14		3.0
RBW-15 0110-0120	92		1.7
RBW-15 0120-0130	<5	<5	0.5
RBW-15 0130-0140	<5		<0.5
RBW-15 0140-0150	21		0.6
RBW-15 0150-0160	11		0.8
RBW-15 0160-0170	<5		<0.5
RBW-15 0170-0180	<5		<0.5
RBW-15 0180-0190	92		1.2
RBW-15 0190-0200	263		2.4
RBW-15 0200-0210	275		4.0
RBW-15 0210-0220	52		2.1
RBW-15 0220-0230	26		1.1
RBW-15 0230-0240	14		1.0
RBW-15 0240-0250	12		0.5

AMERICAN ASSAY LABORATORIES

PROVISIONAL REPORT SP036052

CLIENT : HECLA MINING CO.
PROJECT : ROSEBUD
REFERENCE : RBW-15

REPORTED : 6 NOV 1995

SAMPLES	Au	Au(R)	Ag
RBW-15 0250-0260	<5		<0.5
RBW-15 0260-0270	<5		<0.5
RBW-15 0270-0280	<5		<0.5
RBW-15 0280-0290	24		1.3
RBW-15 0290-0300	18		1.1
RBW-15 0300-0310	<5		0.5
RBW-15 0310-0320	<5		<0.5
RBW-15 0320-0330	<5		0.7
RBW-15 0330-0340	<5		<0.5
RBW-15 0340-0350	13		1.2
RBW-15 0350-0360	<5		0.8
RBW-15 0360-0370	<5		<0.5
RBW-15 0370-0380	<5		<0.5
RBW-15 0380-0390	<5		<0.5
RBW-15 0390-0400	<5		<0.5
RBW-15 0400-0410	<5		<0.5
RBW-15 0410-0420	<5		<0.5
RBW-15 0420-0430	<5		<0.5
RBW-15 0430-0440	<5		<0.5
RBW-15 0440-0450	<5		<0.5
RBW-15 0450-0460	<5		<0.5
RBW-15 0460-0470	<5		<0.5
RBW-15 0470-0480	<5		<0.5
RBW-15 0480-0490	<5		<0.5
RBW-15 0490-0500	<5	<5	<0.5

AMERICAN ASSAY LABORATORIES

PROVISIONAL REPORT SP036052

CLIENT : HECLA MINING CO.
PROJECT : ROSEBUD
REFERENCE : RBW-15

REPORTED : 6 NOV 1995

SAMPLES	Au	Au(R)	Ag
RBW-15 0500-0510	<5		<0.5
RBW-15 0510-0520	<5		<0.5
RBW-15 0520-0530	<5		<0.5
RBW-15 0530-0540	<5		<0.5
RBW-15 0540-0550	<5		<0.5
RBW-15 0550-0560	<5		<0.5
RBW-15 0560-0570	<5		<0.5
RBW-15 0570-0580	<5		<0.5
RBW-15 0580-0590	<5		<0.5
RBW-15 0590-0600	<5		<0.5
RBW-15 0600-0610	<5		<0.5
RBW-15 0610-0620	<5		<0.5
RBW-15 0620-0630	<5		<0.5
RBW-15 0630-0640	<5		<0.5
RBW-15 0640-0650	<5		<0.5
RBW-15 0650-0660	<5	<5	<0.5
RBW-15 0660-0670	<5		<0.5
RBW-15 0670-0680	<5		<0.5
RBW-15 0680-0690	<5		<0.5
RBW-15 0690-0700	<5		0.5
RBW-15 0700-0710	<5		<0.5
RBW-15 0710-0720	<5	<5	<0.5
RBW-15 0720-0730	<5		<0.5
RBW-15 0730-0740	32		1.2
RBW-15 0740-0750	16		0.8

AMERICAN ASSAY LABORATORIES

PROVISIONAL REPORT SP036052

CLIENT : HECLA MINING CO.
PROJECT : ROSEBUD
REFERENCE : RBW-15

REPORTED : 6 NOV 1995

SAMPLES	AU	AU(R)	AG
RBW-15 0750-0760	<5		0.6
RBW-15 0760-0770	26		0.8
RBW-15 0770-0780	20		0.7
RBW-15 0780-0790	20		0.7
RBW-15 0790-0800	15		0.7
RBW-15 0800-0810	34	28	0.9
RBW-15 0810-0820	23		0.7
RBW-15 0820-0830	<5		1.2
RBW-15 0830-0840	20		0.5
RBW-15 0840-0850	10		<0.5
RBW-15 0850-0860	16		<0.5
RBW-15 0860-0870	28		1.0
RBW-15 0870-0880	40		0.7
RBW-15 0880-0890	40		0.7
RBW-15 0890-0900	41		0.5
RBW-15 0900-0910	34		0.6
RBW-15 0910-0920	34		0.6
RBW-15 0920-0930	27		0.6
RBW-15 0930-0940	19		<0.5
RBW-15 0940-0950	8	5	<0.5
RBW-15 0950-0960	10		<0.5
RBW-15 0960-0970	20		<0.5
RBW-15 0970-0980	111		1.0
RBW-15 0980-0990	<5		<0.5
RBW-15 0990-1000	<5		<0.5

AMERICAN ASSAY LABORATORIES

PROVISIONAL REPORT SP036052

CLIENT : HECLA MINING CO.
PROJECT : ROSEBUD
REFERENCE : RBW-15

REPORTED : 6 NOV 1995

SAMPLES	AU	AU(R)	AG
RBW-15 1000-1010	8		<0.5
RBW-15 1010-1020	<5	<5	<0.5
RBW-15 1020-1030	<5		<0.5
RBW-15 1030-1040	<5		<0.5
RBW-15 1040-1050	81		<0.5
RBW-15 1050-1060	48		<0.5
RBW-15 1060-1070	<5		<0.5
RBW-15 1070-1080	9		<0.5
RBW-15 1080-1090	52		0.5
RBW-15 1090-1100	8		<0.5
RBW-15 1100-1110	<5		<0.5
RBW-15 1110-1120	5		<0.5
RBW-15 1120-1130	<5		<0.5
RBW-15 1130-1140	<5		<0.5
RBW-15 1140-1150	<5	<5	<0.5
RBW-15 1150-1160	<5		<0.5
RBW-15 1160-1170	22		1.3
RBW-15 1170-1180	47		1.6
RBW-15 1180-1190	45		1.3
RBW-15 1190-1200	9		1.0
RBW-15 1200-1210	5		1.1
RBW-15 1210-1220	17		0.9
RBW-15 1220-1230	9		<0.5
RBW-15 1230-1240	11	12	0.5
RBW-15 1240-1250	168		1.5

AMERICAN ASSAY LABORATORIES

PROVISIONAL REPORT SP036052

CLIENT : HECLA MINING CO.
PROJECT : ROSEBUD
REFERENCE : RBW-15

REPORTED : 6 NOV 1995

SAMPLES	Au	Au(R)	Ag
RBW-15 1250-1260	<5		0.5
RBW-15 1260-1270	19		0.8
RBW-15 1270-1280	<5		0.7
RBW-15 1280-1290	29		1.0
RBW-15 1290-1300	60		0.6
RBW-15 1300-1310	9		0.8
RBW-15 1310-1320	<5		0.7
RBW-15 1320-1330	5		0.6
RBW-15 1330-1340	<5		0.5
RBW-15 1340-1350	<5		0.7
RBW-15 1350-1360	<5		0.5
RBW-15 1360-1370	112	132	1.1
RBW-15 1370-1380	<5	<5	0.5
RBW-15 1380-1390	7		0.8
RBW-15 1390-1400	14		1.1
