60001952

Mining District File Summary Sheet

DISTRICT	Rosebud
DIST_NO	4010
COUNTY If different from written on document	Pershing
TITLE If not obvious	Rosebud Project underground rib sampling, 1995
AUTHOR	
DATE OF DOC(S)	1995-1996
MULTI_DIST Y / N? Additional Dist_Nos:	
QUAD_NAME	Sulphur 7½'
P_M_C_NAME (mine, claim & company names)	Rosebud Mine; Rosebud Project; Hecla Mining Co
COMMODITY If not obvious	gold; silver
NOTES	Underground rib sampling data; location map; assays; handwritten notes 15p.

Keep docs at about 250 pages if no oversized maps attached
(for every 1 oversized page (>11x17) with text reduce
the amount of pages by ~25)

SS: DD 9/11/08
Initials Date

DB:
Initials Date

SCANNED:
Initials Date

Revised: 1/22/08

ROSEBUD PROJECT UNDERGROUND
RIB SAMPLING, 1995

60001952

4010

6000195 2 4010

Hecla Mining Company - Rosebud Project
1995 Underground Fill-in Drilling Program
Downhole Survey Database

(magnetic declination = 18°W)

file: c:\1234\downhole.wk3
updated: 10/15/95

Hole ID	Section	Station	Downhole Location	Bearing	Azimuth	Inclination	T.D.
D-95-95	975N	18.5	0	S56E	124.0	-11.0	150
D-96-95	975N	18.5	0	S56.5E	123.5	12.0	140
D-97-95	975N	18.5					
D-98-95	950N	18					
D-99-95	925N	17.5					
D-100-95	925N	17.5					
D-101-95	925N	17.5					
D-102-95	900N	17					
D-103-95	900N	17					
D-104-95	875N	16.5	0	S68E	112.0	-65.0	200
D-105-95	875N	16.5	0	S64.5E	115.5	-35.0	
			100	S64.5E	115.5	-35.0	
			200	S66E	114.0	-35.0	200
D-106-95	875N	16.5	0	S57E	123.0	-10.0	
			140	S55E	125.0	-10.5	
			286	S55.5E	124.5	-11.0	286
D-107-95	875N	16.5	0	S56E	124.0	7.5	
			100	S56.5E	123.5	7.0	
			206	S57E	123.0	7.0	206
D-108-95	875N	16.5	0	S66E	114.0	39.5	
			60	S56E	124.0	39.0	130
D-109-95	850N	16					
D-110-95	850N	16					
D-111-95	850N	16					
D-112-95	825N	15.5	0	S47E	133.0	-79.5	200
D-113-95	825N	15.5	0	S56.5E	123.5	-23.0	
			110	S56E	124.0	-23.5	
			215	S57E	123.0	-24.0	220
D-114-95	825N	15.5	10	S54.5E	125.5	5.0	
			150	S56.5E	123.5	5.0	
			295	S56E	124.0	5.0	300
D-115-95	825N	15.5	0	S58E	122.0	35.0	
			75	S56E	124.0	35.0	
			150	S57E	123.0	35.0	150
D-116-95	800N	15					
D-117-95	800N	15					
D-118-95	775N	14.5	15	N57W	327.0	-86.0	180
D-119-95	775N	14.5	0	S57E	123.0	-66.0	130
D-120-95	775N	14.5	0	S55.5E	124.5	-21.0	
			75	S56.5E	123.5	-21.5	
			150	S57E	123.0	-22.0	150
D-121-95	775N	14.5	0	S55E	125.0	-3.0	
			100	S56E	124.0	-4.0	
			200	S56E	124.0	-4.0	200
D-122-95	775N	14.5	15	S56.5E	123.5	51.0	
			90	S57E	123.0	51.5	
			175	S58E	122.0	50.5	180
D-123-95	775N	14.5	0	S56.5E	123.5	64.0	
			65	S55.5E	124.5	64.0	
			136	S57E	123.0	64.5	136
D-124-95	750N	14					
D-125-95	725N	13.5	0	S58.5E	121.5	-56.0	
			50	S57.5E	122.5	-56.0	
			100	S57.5E	122.5	-56.0	100
D-126-95	725N	13.5	15	S59.5E	120.5	19.5	
			120	S58.5E	121.5	19.0	
			235	S60E	120.0	18.5	240
D-127-95	725N	13.5	0	S57.5E	122.5	39.0	
			85	S59.5E	120.5	39.0	
			176	S60E	120.0	38.5	176
D-128-95	700N	13					
D-129-95	675N	12.5					
D-130-95	675N	12.5					
D-131-95	625N	11.5					

STATION 11 1/2 - 625 N

✓ D-131-95 : 240' @ +24° ✓

STATION 12 - 650 N

NO DRILLING

STATION 12 1/2 - 675 N

✓ D-129-95 : 300' @ +5° ✓
✓ D-130-95 : 220' @ +24° ✓

STATION 13 - 700N

✓ D-128-95 : 250' @ +11°

STATION 13 1/2 - 725 N

✓ D-125-95 : 100' @ -55°
✓ D-126-95 : 240' @ +20°
✓ D-127-95 : 170' @ +40°

STATION 14 - 750 N

D - 124 - 95 : 250' @ +10°

STATION 14 ½ - 775 N

D - 118 - 95 : 190' @ -85° → opposite direction than the rest of the holes
D - 119 - 95 : 130' @ -65°
D - 120 - 95 : 150' @ -21°
D - 121 - 95 : 200' @ -3°
D - 122 - 95 : 180' @ +52°
D - 123 - 95 : 130' @ +65°

STATION 15 - 800 N

D - 116 - 95 : 120' @ -21°
D - 117 - 95 : 250' @ +11°

STATION 15½ - 825 N

D - 112 - 95 : 200' @ -80°
D - 113 - 95 : 220' @ -23°
D - 114 - 95 : 300' @ +5°
D - 115 - 95 : 150' @ +35°

STATION 16 - 850N

D-109-95 : 140' @ -60°
D-110-95 : 270' @ -8°
D-111-95 : 150' @ +17°

STATION 16½ - 875 N

D-104-95 : 200' @ -65°
D-105-95 : 200' @ -35°
D-106-95 : 280' @ -10°
D-107-95 : 200' @ +8°
D-108-95 : 130' @ +40°

STATION 17 - 900 N (cross-cut)

D-102-95 : 240' @ -25°
D-103-95 : 150' @ +18°

STATION 17½ - 925 N

D-99-95 : 150' @ -37°
D-100-95 : 250' @ -13°
D-101-95 : 150' @ +20°

STATION 18 - 950 N

D-98-95 : 120' @ +13°

STATION 18 ½ - 975 N

D-95-95 : 150' @ -12°
D-96-95 : 140' @ +12°
D-97-95 : 110' @ +43°

ROSEBUD PROJECT UNDERGROUND RIB SAMPLING, 1995

SAMPLE #	LOCATION	FROM	TO	MAP POINTS	RIB	GOLD OPT	SILVER OPT	SAMPLE DESCRIPTION
5502	CROSS-CUT #17	83.0	86.2	MP2-MP3	RIGHT	0.001	0.06	ARGILIC ALTERATION ZONE
5508	CROSS-CUT #17	80.4	76.0	MP2-MP3	RIGHT	0.003	0.04	LAPILLI TUFF BRECCIA W/MINOR SIO2.
5503	CROSS-CUT #17	80.4	83.0	MP2-MP3	RIGHT	0.001	0.05	ARGILIC ALTERATION ZONE
5509	CROSS-CUT #17	72.0	76.0	MP2-MP3	RIGHT	0.004	0.04	LAPILLI TUFF BRECCIA W/MOD SIO2
5510	CROSS-CUT #17	72.0	67.0	MP2-MP3	RIGHT	0.005	0.06	MOD PLANAR LAMINATED ASH TUFF.
5511	CROSS-CUT #17	67.0	62.0	MP2-MP3	RIGHT	0.004	0.05	MOD PLANAR LAMINATED ASH TUFF.
5513	CROSS-CUT #17	62.0	57.0	MP2-MP3	RIGHT UP	0.006	0.03	LSTWB
5512	CROSS-CUT #17	62.0	57.0	MP2-MP3	RIGHT LOW	0.004	0.05	MOD PLANAR LAMINATED ASH TUFF.
5526	CROSS-CUT #17	52.0	57.0	MP2-MP3	RIGHT	0.005	0.08	LST PROP
5527	CROSS-CUT #17	46.2	52.0	MP2-MP3	RIGHT	0.003	0.04	LST PROP
5528	CROSS-CUT #17	43.0	46.2	MP2-MP3	RIGHT	0.002	0.03	WHITE CLAY FRACTURE ZONE. ASSOC WITH 5521 LEFT RIB.
5537	CROSS-CUT #17	39.0	43.0	MP2-MP3	RIGHT UP	0.002	0.04	PLANAR LAM ASH TUFF, HARD, SIO2?, ASSOC W/5522 LEFT RIB
5529	CROSS-CUT #17	39.0	43.0	MP2-MP3	RIGHT LOW	0.003	0.03	MOD PLANAR LAM ASH TUFF, MIN WHITE CLAY, COMMON MARC VEINLETS.
5530	CROSS-CUT #17	36.7	39.0	MP2-MP3	RIGHT	0.005	0.04	MOD PLANAR LAM ASH TUFF
5531	CROSS-CUT #17	36.2	36.7	MP2-MP3	RIGHT	0.034	0.19	WHITE CLAY + SIO2 BX ZONE ASSOC W/5525 LEFT RIB
5532	CROSS-CUT #17	33.5	36.2	MP2-MP3	RIGHT	0.058	0.42	CS VOL BX
5533	CROSS-CUT #17	32.4	33.5	MP2-MP3	RIGHT	0.035	0.23	WHITE CLAY + SIO2 BX
5535	CROSS-CUT #17	28.8	32.4	MP2-MP3	RIGHT UP	0.036	0.11	MOD PLANAR LAM ASH TUFF, PROP, ASSOC W/5538 LEFT RIB
5534	CROSS-CUT #17	28.8	32.4	MP2-MP3	RIGHT LOW	0.026	0.18	MS LAPILLI VOLC BX
5551	CROSS-CUT #17	27.8	28.8	MP2-MP3	RIGHT	0.006	0.05	MS LAPILLI BX
5552	CROSS-CUT #17	27.0	27.8	MP2-MP3	RIGHT	0.022	0.40	NORMAL DIP SLIP FAULT, TT=0.5", ASSOC W/ 5544 LEFT RIB
5553	CROSS-CUT #17	22.7	27.0	MP2-MP3	RIGHT	0.204	0.29	MS LAPILLI BX
5554	CROSS-CUT #17	21.5	22.7	MP2-MP3	RIGHT	0.082	0.10	SMALL FAULT, TT=6.0", ASSOC ? W/5546 LEFT RIB
5555	CROSS-CUT #17	18.6	21.5	MP2-MP3	RIGHT	0.020	0.09	CREAM CLAY CLAST BX W/CHLOR STKWK, TT=1.5-2.5'
5556	CROSS-CUT #17	14.7	18.6	MP2-MP3	RIGHT	0.277	0.71	LST, PROP
5557	CROSS-CUT #17	14.7	14.2	MP2-MP3	RIGHT	0.885	2.00	SMALL FAULT, TT=0.5-2.0"
5559	CROSS-CUT #17	10.3	12.4	MP2-MP3	RIGHT LOW	0.250	0.49	C-G WEAKLY LAM ASH TUFF
5558	CROSS-CUT #17	10.3	14.2	MP2-MP3	RIGHT	1.517	1.80	LST, POT, ASSOC W/ 5550 LEFT RIB
5560	CROSS-CUT #17	8.3	10.3	MP2-MP3	RIGHT	0.718	0.85	C-G WEAKLY LAM ASH TUFF
5569	CROSS-CUT #17	8.3	10.3	MP2-MP3	RIGHT	1.923	3.21	SULFIDE AND QUARTZ VEINLETS "ONLY" (SAME SITE AS 5560)
5561	CROSS-CUT #17	7.8	8.3	MP2-MP3	RIGHT	4.041	7.82	OPEN SPACE FAULT-EXT FRACT W/ MARC + BARITE, TT=1-6"
5562	CROSS-CUT #17	4.5	7.8	MP2-MP3	RIGHT	0.609	0.85	F-G TO C-G PLANAR LAM ASH TUFF
5567	CROSS-CUT #17	4.5	7.8	MP2-MP3	RIGHT	16.607	32.50	SULFIDE VEINLETS "ONLY" (SAME SITE AS 5562)
5568	CROSS-CUT #17	4.5	7.8	MP2-MP3	RIGHT	0.175	2.60	ROCK W/ NO SULFIDE VEINLETS (SAME SITE AS 5562)
5563	CROSS-CUT #17	0.0	4.5	MP2-MP3	RIGHT	15.378	17.00	F-G TO C-G PLANAR LAM ASH TUFF
5564	CROSS-CUT #17	0.0	4.5	MP2-MP3	RIGHT	48.616	27.40	MARCASITE-SULFIDE FRACTURE FILL "ONLY" (SAME SITE AS 5563)
5565	CROSS-CUT #17	0.0	4.5	MP2-MP3	RIGHT	0.260	2.80	WALL ROCK "ONLY" W/ NO SULFIDE VEINLETS (SAME SITE AS 5563)
5566	CROSS-CUT #17	0.0	4.5	MP2-MP3	RIGHT	6.458	26.00	MOST REPRESENTATIVE SAMPLE FOR AREA COVERED BY 5563
5588	CROSS-CUT #17	71.5	75.0	MP1-MP2	RIGHT UP	8.070	12.60	FAULT ASSOC W/ 5579 LEFT RIB, TT=4"
5587	CROSS-CUT #17	71.5	75.0	MP1-MP2	RIGHT LOW	11.668	15.20	F-G PLANAR LAM ASH TUFF, PROP
5590	CROSS-CUT #17	71.5	75.0	MP1-MP2	RIGHT	93.340	26.80	SULFIDE VEINLETS "ONLY" (SAME SITE AS 5587)
5591	CROSS-CUT #17	71.5	75.0	MP1-MP2	RIGHT	0.386	1.28	ROCK "ONLY" W/ NO SULFIDE VEINLETS (SAME SITE AS 5587)
5589	CROSS-CUT #17	67.7	71.5	MP1-MP2	RIGHT	0.863	2.07	F-G PLANAR LAM ASH TUFF
5595	CROSS-CUT #17	63.0	67.5	MP1-MP2	RIGHT	0.116	1.46	F-G MASSIVE ASH TUFF
5596	CROSS-CUT #17	59.6	63.0	MP1-MP2	RIGHT	0.340	4.73	F-G MASSIVE ASH TUFF
5597	CROSS-CUT #17	56.0	59.6	MP1-MP2	RIGHT	0.059	0.46	F-G MASSIVE ASH TUFF
5598	CROSS-CUT #17	51.0	56.0	MP1-MP2	RIGHT	0.091	1.13	MS, MONO?, VOLC BX
5599	CROSS-CUT #17	48.0	51.0	MP1-MP2	RIGHT	0.035	0.58	MS, MONO?, VOLC BX

SAMPLE #	LOCATION	FROM	TO	MAP POINTS	RIB	GOLD OPT	SILVER OPT	SAMPLE DESCRIPTION
5600	CROSS-CUT #17	43.5	48.0	MP1-MP2	RIGHT	0.043	0.28	MS, MONO?, VOLC BX
5601	CROSS-CUT #17	43.2	43.5	MP1-MP2	RIGHT	1.540	1.37	LOW ANGLE REVERSE FAULT W/ LATER NORMAL MOVEMENT
5602	CROSS-CUT #17	38.1	43.2	MP1-MP2	RIGHT	9.139	14.20	HET, MS, VOLC BX, SIO2 + SULF VEINLETS.
5614	CROSS-CUT #17	38.1	43.2	MP1-MP2	RIGHT	217.800	127.00	SULFIDE + CACO3 VEINLETS "ONLY" (SAME SITE AS 5602)
5615	CROSS-CUT #17	38.1	43.2	MP1-MP2	RIGHT	0.446	1.28	ROCK W/ NO CACO3 + SULFIDE VEINING (SAME SITE AS 5602)
5603	CROSS-CUT #17	34.4	38.1	MP1-MP2	RIGHT	3.422	3.59	HET, MS, VOLC BX, SIO2 + SULF VEINLETS. (HIGHER DENSITY THAN 5602)
5616	CROSS-CUT #17	34.4	38.1	MP1-MP2	RIGHT	10.832	13.80	SULFIDE VEINLETS "ONLY" (SAME SITE AS 5603)
5617	CROSS-CUT #17	34.4	38.1	MP1-MP2	RIGHT	0.142	0.34	CLAST ROCK "ONLY" (SAME SITE AS 5603)
5618	CROSS-CUT #17	34.4	38.1	MP1-MP2	RIGHT	0.068	0.09	PINK MATRIX "ONLY" (SAME SITE AS 5603)
5604	CROSS-CUT #17	31.7	34.4	MP1-MP2	RIGHT	0.718	0.68	HET, MS, VOLC BX, SIO2 + SULF VEINLETS. (HIGHER DENSITY THAN 5602)
5619	CROSS-CUT #17	31.7	34.4	MP1-MP2	RIGHT	13.851	14.50	VEINING "ONLY" (SAME SITE AS 5604)
5620	CROSS-CUT #17	31.7	34.4	MP1-MP2	RIGHT	1.047	1.15	CLAST ROCK "ONLY" (SAME SITE AS 5604)
5621	CROSS-CUT #17	31.7	34.4	MP1-MP2	RIGHT	0.012	0.07	MATRIX "ONLY" (SAME SITE AS 5604)
5605	CROSS-CUT #17	31.5	31.7	MP1-MP2	RIGHT	55.420	20.80	MARC + SIO2 VEINLET, TT = 1-3" WIDE
5606	CROSS-CUT #17	28.7	31.5	MP1-MP2	RIGHT	0.379	0.92	HET, MS, VOLC BX, SIO2+CACO3+SULFIDE VEINLETS (LOWER DENSITY THAN 5603)
5660	CROSS-CUT #17	28.7	31.5	MP1-MP2	RIGHT	0.063	0.11	ROCK "ONLY" W/ NO SULFIDE VEINLETS (SAME SITE AS 5606)
5607	CROSS-CUT #17	25.5	28.7	MP1-MP2	RIGHT	0.084	0.47	HET, MS, VOLC BX, SIO2+CACO3+SULFIDE VEINLETS (LOWER DENSITY THAN 5603)
5661	CROSS-CUT #17	25.5	28.7	MP1-MP2	RIGHT	0.023	0.09	ROCK "ONLY" W/ NO SULFIDE VEINLETS (SAME SITE AS 5607)
5608	CROSS-CUT #17	24.8	25.5	MP1-MP2	RIGHT	0.180	0.64	CONTACT ZONE BETWEEN HET, MS, VOLC BX AND F-G MASSIVE ASH TUFF
5622	CROSS-CUT #17	21.0	24.8	MP1-MP2	RIGHT	0.064	0.24	F-G MASSIVE PINK ASH TUFF
5662	CROSS-CUT #17	21.0	24.8	MP1-MP2	RIGHT	0.011	0.10	ROCK "ONLY" W/ NO SULFIDE VEINLETS (SAME SITE AS 5622
5623	CROSS-CUT #17	17.0	21.0	MP1-MP2	RIGHT	0.129	0.46	F-G MASSIVE PINK ASH TUFF ALTERED BE SMALL FAULT
5624	CROSS-CUT #17	11.7	17.0	MP1-MP2	RIGHT	0.498	1.45	HET, MS, VOLC BX, MOD SULFIDE + WHITE CLAY VEINLETS + SIO2
5625	CROSS-CUT #17	7.4	11.7	MP1-MP2	RIGHT	0.450	0.98	HET, MS, VOLC BX W/ COMMON WHITE CLAY + MARC VEINLETS + SIO2
5640	CROSS-CUT #17	7.4	11.7	MP1-MP2	RIGHT	5.612	15.40	WHITE CLAY + MARC "ONLY" (SAME SITE AS 5625)
5626	CROSS-CUT #17	5.0	7.4	MP1-MP2	RIGHT	0.784	3.16	HET, MS, VOLC BX W/ MINOR MARC + CLAY VEINLETS + SIO2
5627	CROSS-CUT #17	0.0	5.0	MP1-MP2	RIGHT	0.179	3.30	HET, MS, VOLC BX W/ COMMON WHITE CLAY + MARC VEINLETS + SIO2
5668	CROSS-CUT #17	84.3	89.2	MP0-MP1	RIGHT	0.160	0.62	F-G PLANAR LAM ASH TUFF
5669	CROSS-CUT #17	80.7	84.3	MP0-MP1	RIGHT	0.141	0.55	F-G PLANAR LAM ASH TUFF
5670	CROSS-CUT #17	75.8	80.7	MP0-MP1	RIGHT	0.100	0.28	F-G PLANAR LAM ASH TUFF
5671	CROSS-CUT #17	72.0	75.8	MP0-MP1	RIGHT	0.137	0.19	F-G PLANAR LAM ASH TUFF
5672	CROSS-CUT #17	70.8	72.0	MP0-MP1	RIGHT	0.268	0.29	SILICIFIED BX IN HINGE OF FOLD, F-G PLANAR LAM ASH TUFF
5673	CROSS-CUT #17	67.1	70.8	MP0-MP1	RIGHT	0.132	0.43	F-G PLANAR LAM ASH TUFF
5674	CROSS-CUT #17	64.3	67.1	MP0-MP1	RIGHT	0.221	0.37	F-G PLANAR LAM ASH TUFF
5675	CROSS-CUT #17	63.3	64.3	MP0-MP1	RIGHT	0.295	0.60	MINOR FAULT W/ WHITE CLAY + SULFIDES, ASSOC W/ 5689, TT=1-3"
5676	CROSS-CUT #17	61.3	63.3	MP0-MP1	RIGHT	0.009	0.08	F-G PLANAR LAM ASH TUFF
5677	CROSS-CUT #17	59.8	61.3	MP0-MP1	RIGHT	0.004	0.05	HET, MS, VOLC BX.
5678	CROSS-CUT #17	55.9	59.8	MP0-MP1	RIGHT	0.027	0.11	HET, MS, VOLC BX.
5705	CROSS-CUT #17	50.4	55.9	MP0-MP1	RIGHT	0.004	0.07	HET, MS, VOLC BX.
5706	CROSS-CUT #17	45.2	50.4	MP0-MP1	RIGHT	0.010	0.10	HET, MS, VOLC BX.
5707	CROSS-CUT #17	41.4	45.2	MP0-MP1	RIGHT	0.011	0.15	HET, MS, VOLC BX.
5708	CROSS-CUT #17	39.2	41.4	MP0-MP1	RIGHT	0.014	0.20	FRACTURE ZONE, W/ WHITE CLAY + MARC + BARITE. ASSOC W/ 5697 LEFT RIB.
5715	CROSS-CUT #17	39.2	41.4	MP0-MP1	RIGHT	0.010	0.58	WHITE CLAY + BARITE + MARC "ONLY". (SAME SITE AS 5708)
5709	CROSS-CUT #17	36.0	39.2	MP0-MP1	RIGHT	0.005	0.08	HET, MS, VOLC BX.
5710	CROSS-CUT #17	33.0	36.0	MP0-MP1	RIGHT	0.008	0.10	HET, MS, VOLC BX.
5711	CROSS-CUT #17	28.5	33.0	MP0-MP1	RIGHT	0.008	0.09	HET, MS, VOLC BX, W/ HIGH FRACTURE DENSITY W/ MARC + WHITE CLAY+/- BARITE.
5712	CROSS-CUT #17	24.0	28.5	MP0-MP1	RIGHT	0.009	0.09	HET, MS, VOLC BX.
5713	CROSS-CUT #17	21.9	24.0	MP0-MP1	RIGHT	0.008	0.11	FAULT/FRACTURE ZONE W/ WHITE CLAY + MARC + BARITE. ASSOC W/ 5702 LEFT RIB.
5714	CROSS-CUT #17	17.5	21.9	MP0-MP1	RIGHT	0.013	0.14	HET, MS, VOLC BX, W/ HIGH FRACTURE DENSITY W/ MARC + WHITE CLAY.
5501	CROSS-CUT #17	81.2	83.7	MP2-MP3	LEFT	0.004	0.07	ARGILIC ALTERATION ZONE
5505	CROSS-CUT #17	77.0	81.2	MP2-MP3	LEFT UP	0.006	0.05	MOD PLANAR LAMINATED TUFF. ARGILLIZED AML.
5504	CROSS-CUT #17	77.0	81.2	MP2-MP3	LEFT LOW	0.002	0.05	F-G LAPILLI TUFF BRECCIA

SAMPLE #	LOCATION	FROM	TO	MAP POINTS	RIB	GOLD OPT	SILVER OPT	SAMPLE DESCRIPTION
5506	CROSS-CUT #17	72.8	77.0	MP2-MP3	LEFT	0.001	0.03	F-G LAPILLI TUFF BRECCIA. MIN-MOD SIO2 FLOODING.
5507	CROSS-CUT #17	70.3	72.8	MP2-MP3	LEFT	0.008	0.04	SILICIFIED STRUCTURE AND SILICA HALO W/ MARCASITE.
5514	CROSS-CUT #17	65.0	70.3	MP2-MP3	LEFT	0.010	0.05	LSTWB ? W/MINOR LAMINATIONS.
5516	CROSS-CUT #17	60.0	65.0	MP2-MP3	LEFT UP	0.002	0.04	LSTWB
5515	CROSS-CUT #17	60.0	65.0	MP2-MP3	LEFT LOW	0.005	0.06	MOD PLANAR LAMINATED ASH TUFF.
5518	CROSS-CUT #17	55.0	60.0	MP2-MP3	LEFT UP	0.012	0.04	LSTWB
5517	CROSS-CUT #17	55.0	60.0	MP2-MP3	LEFT LOW	0.006	0.05	MOD PLANAR LAM ASH TUFF, SOFT, PROP+ARG
5520	CROSS-CUT #17	50.0	55.0	MP2-MP3	LEFT UP	0.016	0.02	LSTWB
5519	CROSS-CUT #17	50.0	55.0	MP2-MP3	LEFT LOW	0.005	0.04	MOD PLANAR LAMINATED ASH TUFF.
5521	CROSS-CUT #17	48.0	50.0	MP2-MP3	LEFT	0.012	0.03	2" WIDE FRACTURE ZONE WITH WHITE CLAY + SIO2
5522	CROSS-CUT #17	43.0	48.0	MP2-MP3	LEFT	0.002	0.00	PLANAR LAM ASH TUFF, HARD, SILICIFIED?
5523	CROSS-CUT #17	40.0	43.0	MP2-MP3	LEFT	0.167	0.12	MATRIX SUP LAPILLI-BLOCK BRECCIA. INCREASE IN MARK VEINLETS
5524	CROSS-CUT #17	36.7	40.0	MP2-MP3	LEFT	0.005	0.03	MATRIX SUP LAPILLI-BLOCK BRECCIA. INCREASE IN MARK VEINLETS
5536	CROSS-CUT #17	33.9	34.2	MP2-MP3	LEFT	0.064	13.00	VUG HOLE FILLED WITH SERICITIC? CLAY
5525	CROSS-CUT #17	33.0	36.7	MP2-MP3	LEFT	0.018	0.63	WHITE CLAY + SIO2 STOCKWORK BRECCIA. ABUNDANT WHITE CLAY.
5538	CROSS-CUT #17	28.0	33.0	MP2-MP3	LEFT UP	0.036	0.13	MOD PLANAR LAM ASH TUFF, PROP, ASSOC W/5535 RIGHT RIB
5539	CROSS-CUT #17	26.1	30.4	MP2-MP3	LEFT LOW	0.043	0.14	VOLC BX, POT, ASSOC W/5534
5540	CROSS-CUT #17	23.0	28.0	MP2-MP3	LEFT UP	0.032	0.12	MOD PLANAR LAM ASH TUFF, PROP
5541	CROSS-CUT #17	21.4	26.1	MP2-MP3	LEFT LOW	0.024	0.07	VOLC BX, POT
5542	CROSS-CUT #17	20.9	21.4	MP2-MP3	LEFT	0.008	0.06	MARCASITE FRACTURE
5543	CROSS-CUT #17	19.3	20.9	MP2-MP3	LEFT	0.008	0.05	VOLC BX, POT
5544	CROSS-CUT #17	19.0	19.3	MP2-MP3	LEFT	0.028	0.05	FAULT ZONE, NORMAL DIP SLIP
5545	CROSS-CUT #17	17.1	19.0	MP2-MP3	LEFT	0.036	0.05	MS VOLC BX, PROP
5546	CROSS-CUT #17	16.8	17.1	MP2-MP3	LEFT	0.010	0.14	MARCASITE VEINLET, UP TO 0.5" WIDE
5547	CROSS-CUT #17	12.2	16.8	MP2-MP3	LEFT	0.018	0.08	MS VOLC BX, PROP
5548	CROSS-CUT #17	10.8	12.2	MP2-MP3	LEFT	0.014	0.67	MS VOLC BX, LST CLASTS, ASSOC W/ FAULT?
5549	CROSS-CUT #17	8.0	10.8	MP2-MP3	LEFT	0.048	0.17	LST, PROP
5550	CROSS-CUT #17	5.5	8.0	MP2-MP3	LEFT UP	0.166	0.59	LST, PROP, W/ WHITE CLAY AND MARC FRACTURES
5573	CROSS-CUT #17	4.7	6.0	MP2-MP3	LEFT UP	0.467	2.68	LST PROP
5572	CROSS-CUT #17	4.3	5.3	MP2-MP3	LEFT UP	0.251	2.98	SMALL FAULT W/ WHITE CLAY, LST PROP, ASSOC? W/ 5561
5571	CROSS-CUT #17	4.3	4.9	MP2-MP3	LEFT LOW	0.205	0.42	SMALL FAULT W/ WHITE CLAY, LAM ASH TUFF, ASSOC ? W/ 5561
5570	CROSS-CUT #17	3.0	6.4	MP2-MP3	LEFT LOW	0.245	0.71	F-G TO C-G PLANAR LAM ASH TUFF
5574	CROSS-CUT #17	0.0	4.7	MP2-MP3	LEFT	0.388	0.42	F-G TO C-G PLANAR LAM ASH TUFF, POT
5575	CROSS-CUT #17	73.6	77.8	MP1-MP2	LEFT	0.215	1.01	C-G LAM ASH TUFF, POT
5576	CROSS-CUT #17	70.4	73.6	MP1-MP2	LEFT	0.602	2.28	F-G TO C-G ASH TUFF, PROP
5577	CROSS-CUT #17	66.4	70.4	MP1-MP2	LEFT LOW	0.788	1.73	F-G TO C-G PLANAR LAM ASH TUFF, PROP
5579	CROSS-CUT #17	65.6	66.4	MP1-MP2	LEFT	7.088	15.90	FAULT ZONE, TT=0.5-3.0"
5578	CROSS-CUT #17	64.4	66.4	MP1-MP2	LEFT MID	6.941	13.20	F-G TO C-G ASH TUFF, PROP, HIGH DENSITY CACO3 + MARC FRACTURES
5592	CROSS-CUT #17	64.4	66.4	MP1-MP2	LEFT	157.500	34.70	LARGE 1" FRACTURE FILLED W/ MARC +/- PYRITE, +SIO2 (SAME SITE AS 5578)
5593	CROSS-CUT #17	64.4	66.4	MP1-MP2	LEFT	18.080	24.80	LARGE CACO3 + MARC + WHITE CLAY FRACTURE, (SAME SITE AS 5578), TT=2-3"
5594	CROSS-CUT #17	64.4	66.4	MP1-MP2	LEFT	0.757	1.98	ROCK "ONLY" W/ NO CACO3 OR MARC VEINLETS (SAME SITE AS 5578
5580	CROSS-CUT #17	62.4	66.4	MP1-MP2	LEFT UP	0.761	7.59	F-G TO C-G MIN PLASNAR LAM ASH TUFF, PROP + , POT +/-
5581	CROSS-CUT #17	60.0	65.6	MP1-MP2	LEFT	0.743	6.77	F-G TO C-G ASH TUFF, PROP
5582	CROSS-CUT #17	55.0	60.0	MP1-MP2	LEFT	0.474	10.60	F-G MASSIVE ASHT TUFF, PROP+, POT+
5583	CROSS-CUT #17	50.0	55.0	MP1-MP2	LEFT	0.924	4.35	F-G MASSIVE ASHT TUFF, PROP+, POT+
5584	CROSS-CUT #17	46.0	50.0	MP1-MP2	LEFT	0.720	4.64	F-G MASSIVE ASHT TUFF, PROP+, POT+
5585	CROSS-CUT #17	43.8	46.0	MP1-MP2	LEFT	0.368	6.83	MS VOLC BX
5586	CROSS-CUT #17	43.4	43.8	MP1-MP2	LEFT	0.230	0.71	REVERSE FAULT W/ LATER DEXTRAL MOVEMENT, TT=1-4"
5609	CROSS-CUT #17	41.6	43.4	MP1-MP2	LEFT	1.546	6.57	HET, MS, VOLC BX, MINOR SULFIDE AND CACO3 VEINLETS
5610	CROSS-CUT #17	38.5	41.6	MP1-MP2	LEFT	0.391	0.32	HET, MS, VOLC BX W/ COMMON SIO2 + CACO3 + SULFIDE VEINLETS
5611	CROSS-CUT #17	35.4	38.5	MP1-MP2	LEFT	0.032	0.51	HET, MS, VOLC BX W/ COMMON SIO2 + CACO3 + SULFIDE VEINLETS
5663	CROSS-CUT #17	35.4	38.5	MP1-MP2	LEFT	1.181	4.40	SULFIDE VEINLETS +/- WHITE CLAY + SIO2 "ONLY" (SAME SITE AS 5611)

SAMPLE #	LOCATION	FROM	TO	MAP POINTS	RIB	GOLD OPT	SILVER OPT	SAMPLE DESCRIPTION
5664	CROSS-CUT #17	35.4	38.5	MP1-MP2	LEFT	0.017	0.10	CLASTS "ONLY" W/ NO SULFIDE VEINLETS (SAME SITE AS 5611)
5665	CROSS-CUT #17	35.4	38.5	MP1-MP2	LEFT	0.016	0.03	MATRIX "ONLY" (SAME SITE AS 5611)
5612	CROSS-CUT #17	31.3	35.4	MP1-MP2	LEFT	0.093	0.26	HET, MS, VOLC BX W/ MINOR SIO2+CACO3 VEINLETS
5666	CROSS-CUT #17	31.3	35.4	MP1-MP2	LEFT	0.004	0.04	CLASTS "ONLY" (SAME SITE AS 5612)
5667	CROSS-CUT #17	31.3	35.4	MP1-MP2	LEFT	0.006	0.03	MATRIX " ONLY" (SAME SITE AS 5612)
5613	CROSS-CUT #17	29.0	31.3	MP1-MP2	LEFT	1.036	3.33	SIO2 FRACTURE, TT=1"
5628	CROSS-CUT #17	26.5	29.0	MP1-MP2	LEFT	0.170	0.76	HET, MS, VOLC BX. TT=1.4'
5629	CROSS-CUT #17	24.6	26.5	MP1-MP2	LEFT	0.288	4.26	HET, MS, VOLC BX, W/ COMMON WHITE CLAY. TT = 1.6'
5638	CROSS-CUT #17	24.6	26.5	MP1-MP2	LEFT	0.134	2.33	WHITE CLAY + MARC "ONLY" (SAME SITE AS 5629)
5659	CROSS-CUT #17	24.6	26.5	MP1-MP2	LEFT	0.069	0.25	ROCK "ONLY" W/ NO CLAY (SAME SITE AS 5629)
5630	CROSS-CUT #17	22.1	24.6	MP1-MP2	LEFT	0.429	1.46	HET, MS, VOLC BX, W/ MINOR TO MOD MARC VEINLETS
5639	CROSS-CUT #17	22.1	24.6	MP1-MP2	LEFT	2.810	5.57	MARCASITE VEINLETS "ONLY" (SAME SITE AS 5630)
5657	CROSS-CUT #17	22.1	24.6	MP1-MP2	LEFT	0.056	0.17	CLAST MATERIAL "ONLY" (SAME SITE AS 5630)
5658	CROSS-CUT #17	22.1	24.6	MP1-MP2	LEFT	0.105	0.47	MATRIX "ONLY" (SAME SITE AS 5630)
5631	CROSS-CUT #17	20.7	22.1	MP1-MP2	LEFT	1.848	3.80	FRACTURE PLANE W/ COMMON MARC. TT = 1"
5632	CROSS-CUT #17	17.7	20.7	MP1-MP2	LEFT	0.525	1.22	HET, MS, VOLC BX, W/ MINOR MARC VEINLETS
5633	CROSS-CUT #17	13.5	17.7	MP1-MP2	LEFT	0.256	1.21	HET, MS, VOLC BX W/ MINOR WHITE CLAY + MARC VEINLETS
5634	CROSS-CUT #17	10.2	13.5	MP1-MP2	LEFT	0.493	1.79	HET, MS, VOLC BX, W/ MOD COMMON WHITE CLAY + MARC VEINLETS
5635	CROSS-CUT #17	7.6	10.2	MP1-MP2	LEFT	0.892	2.72	HET, MS, VOLC BX, W/ COMMON MARC + WHITE CLAY VEINLETS
5636	CROSS-CUT #17	4.0	7.6	MP1-MP2	LEFT	0.394	1.51	HET, MS, VOLC BX, W/ MINOR TO MOD MARC + WHITE CLAY VEINLETS
5637	CROSS-CUT #17	1.0	4.0	MP1-MP2	LEFT	0.910	1.80	HET, MS, VOLC BX, W/ COMMON MARC + WHITE CLAY VEINLETS
5679	CROSS-CUT #17	86.7	88.4	MP0-MP1	LEFT	0.408	0.40	HET, MS, VOLC BX.
5681	CROSS-CUT #17	83.5	86.7	MP0-MP1	LEFT UP	0.020	0.11	HET, MS, VOLC BX.
5680	CROSS-CUT #17	83.5	86.7	MP0-MP1	LEFT LOW	0.025	0.10	F-G MASSIVE ASH TUFF
5683	CROSS-CUT #17	80.6	83.5	MP0-MP1	LEFT UP	0.006	0.08	HET, MS, VOLC BX.
5682	CROSS-CUT #17	80.6	83.5	MP0-MP1	LEFT LOW	0.011	0.07	F-G MASSIVE ASH TUFF
5685	CROSS-CUT #17	77.0	80.6	MP0-MP1	LEFT UP	0.040	0.05	HET, MS, VOLC BX.
5684	CROSS-CUT #17	77.0	80.6	MP0-MP1	LEFT LOW	0.115	0.07	F-G MASSIVE ASH TUFF
5687	CROSS-CUT #17	73.0	77.0	MP0-MP1	LEFT UP	0.013	0.09	HET, MS, VOLC BX.
5686	CROSS-CUT #17	73.0	77.0	MP0-MP1	LEFT LOW	0.004	0.08	F-G MASSIVE ASH TUFF
5688	CROSS-CUT #17	67.0	73.0	MP0-MP1	LEFT	0.021	0.09	HET, MS, VOLC BX.
5689	CROSS-CUT #17	65.5	67.0	MP0-MP1	LEFT	0.094	0.24	SMALL FAULT ASSOC W/ 5675, 2 SHEARS APPROX 0.5-1" WIDE W/ BX BETWEEN
5691	CROSS-CUT #17	60.8	65.5	MP0-MP1	LEFT UP	0.005	0.08	HET, MS, VOLC BX.
5690	CROSS-CUT #17	60.8	65.5	MP0-MP1	LEFT LOW	0.011	0.13	HET, MS, VOLC BX, CLASTS APPEAR SQUASHED AND STRETCHED.
5692	CROSS-CUT #17	56.3	60.8	MP0-MP1	LEFT	0.007	0.07	HET, MS, VOLC BX.
5693	CROSS-CUT #17	51.7	56.3	MP0-MP1	LEFT	0.029	0.17	HET, MS, VOLC BX.
5694	CROSS-CUT #17	48.0	51.7	MP0-MP1	LEFT	0.005	0.08	HET, MS, VOLC BX.
5695	CROSS-CUT #17	47.0	48.0	MP0-MP1	LEFT	0.039	0.28	HET, MS, VOLC BX, FRACTURE ZONE W/ VUGS, BARITE, WHITE CLAY, MARC.
5696	CROSS-CUT #17	42.3	47.0	MP0-MP1	LEFT	0.002	0.07	HET, MS, VOLC BX.
5697	CROSS-CUT #17	37.5	42.3	MP0-MP1	LEFT	0.009	0.08	HET, MS, VOLC BX.
5698	CROSS-CUT #17	34.1	37.5	MP0-MP1	LEFT	0.035	0.15	HET, MS, VOLC BX.
5699	CROSS-CUT #17	29.7	34.1	MP0-MP1	LEFT	0.009	0.11	HET, MS, VOLC BX.
5700	CROSS-CUT #17	26.4	29.7	MP0-MP1	LEFT	0.011	0.08	HET, MS, VOLC BX.
5701	CROSS-CUT #17	23.6	26.4	MP0-MP1	LEFT	0.022	0.11	HET, MS, VOLC BX W/ INCREASED WHITE CLAY + MARC FRACTURES.
5702	CROSS-CUT #17	21.8	23.6	MP0-MP1	LEFT	0.013	0.10	FRACTURE ZONE, OPEN SPACE, W/ WHITE CLAY + MARC + BARITE + CAC0-3
5703	CROSS-CUT #17	18.4	21.8	MP0-MP1	LEFT	0.012	0.13	HET, MS, VOLC BX.
5704	CROSS-CUT #17	15.0	18.4	MP0-MP1	LEFT	0.007	0.12	HET, MS, VOLC BX.
5723	DECLINE 17-16	40.2	44.6	MP0-MP9	RIGHT	0.006	0.08	HET, MS, VOLC BX, W/ MOD TO COMMON CACO3 + MARC.
5722	DECLINE 17-16	36.6	40.2	MP0-MP9	RIGHT	0.004	0.06	HET, MS, VOLC BX, W/ MINOR CACO3.
5721	DECLINE 17-16	32.3	36.6	MP0-MP9	RIGHT	0.002	0.05	HET, MS, VOLC BX, W/ MINOR CACO3.
5720	DECLINE 17-16	29.0	32.3	MP0-MP9	RIGHT	0.002	0.04	HET, MS, VOLC BX.
5719	DECLINE 17-16	24.1	29.0	MP0-MP9	RIGHT	0.003	0.05	HET, MS, VOLC BX, W/ MOD TO COMMON CACO3 + MARC.

SAMPLE #	LOCATION	FROM	TO	MAP POINTS	RIB	GOLD OPT	SILVER OPT	SAMPLE DESCRIPTION
5728	DECLINE 17-16	24.1	29.0	MP0-MP9	RIGHT	0.054	0.51	CACO3 + MARC VEINLETS "ONLY" (SAME SITE AS 5719)
5718	DECLINE 17-16	20.5	24.1	MP0-MP9	RIGHT	0.001	0.04	HET, MS, VOLC BX.
5717	DECLINE 17-16	17.3	20.5	MP0-MP9	RIGHT	0.001	0.05	HET, MS, VOLC BX, W/ MINOR CACO3.
5716	DECLINE 17-16	13.0	17.3	MP0-MP9	RIGHT	0.007	0.10	HET, MS, VOLC BX, W/ MINOR CACO3.
5738	DECLINE 17-16	38.2	42.6	MP0-MP9	LEFT	0.002	0.02	F-G TO C-G MASSIVE ASH TUFF
5737	DECLINE 17-16	34.0	38.2	MP0-MP9	LEFT	0.003	0.04	HET, MS, VOLC BX.
5736	DECLINE 17-16	30.5	34.0	MP0-MP9	LEFT	0.014	0.09	HET, MS, VOLC BX.
5735	DECLINE 17-16	28.0	30.5	MP0-MP9	LEFT	0.053	0.15	HET, MS, VOLC BX, TT=0.3'.
5734	DECLINE 17-16	23.4	28.0	MP0-MP9	LEFT	0.004	0.05	HET, MS, VOLC BX, TT=1.5'.
5733	DECLINE 17-16	16.4	23.4	MP0-MP9	LEFT	0.007	0.07	HET, MS, VOLC BX, TT=2.5'.
5732	DECLINE 17-16	11.2	16.4	MP0-MP9	LEFT	0.005	0.07	HET, MS, VOLC BX.
5727	DECLINE 16-15	75.5	79.4	MP0-MP9	RIGHT	0.018	0.14	HET, MS, VOLC BX (WELDED), CLASTS ARE SQUASHED AND STRETCHED, TT=1.9'
5726	DECLINE 16-15	71.0	75.5	MP0-MP9	RIGHT	0.012	0.06	HET, MS, VOLC BX.
5725	DECLINE 16-15	67.0	71.0	MP0-MP9	RIGHT	0.001	0.06	HET, MS, VOLC BX.
5724	DECLINE 16-15	64.1	67.0	MP0-MP9	RIGHT	0.010	0.22	HET, MS, VOLC BX.
5746	DECLINE 16-15	73.6	79.4	MP0-MP9	LEFT	0.005	0.04	HET, MS, VOLC BX.
5745	DECLINE 16-15	63.2	73.6	MP0-MP9	LEFT	0.013	0.06	HET, MS, VOLC BX.
5744	DECLINE 16-15	58.8	63.2	MP0-MP9	LEFT	0.003	0.06	HET, MS, VOLC BX W/ MOD COMMON FRACTS W/ CACO3 + MARC, TT=1.9'
5753	DECLINE 16-15	7.0	10.1	MP9-MP12	LEFT	0.040	0.42	HET, MS, VOLC BX (WELDED), CLASTS ARE SQUASHED AND STRETCHED.
5810	DECLINE 15-14	48.2	52.4	MP9-MP12	RIGHT UP	0.001	0.03	VOLC BX W/S&S
5809	DECLINE 15-14	48.2	52.4	MP9-MP12	RIGHT MID	0.001	0.06	LOW ANGLE FAULT/CONTACT TT-1.0-2.0"
5808	DECLINE 15-14	48.2	52.4	MP9-MP12	RIGHT LOW	0.002	0.07	FG PLANAR LAMINATED ASH TUFF
5807	DECLINE 15-14	43.7	48.2	MP9-MP12	RIGHT UP	0.003	0.06	LOW ANGLE FAULT/CONTACT TT-1.0-2.0"
5806	DECLINE 15-14	43.7	48.2	MP9-MP12	RIGHT LOW	0.003	0.05	FG PLANAR LAMINATED ASH TUFF
5805	DECLINE 15-14	38.9	43.7	MP9-MP12	RIGHT UP	0.004	0.06	LOW ANGLE FAULT/CONTACT TT-1.0-2.0"
5804	DECLINE 15-14	38.9	43.7	MP9-MP12	RIGHT LOW	0.004	0.07	FG PLANAR LAMINATED ASH TUFF
5803	DECLINE 15-14	38.7	38.9	MP9-MP12	RIGHT	0.004	0.10	HIGH ANGLE FAULT THAT APPEARS TO OFFSET LOW ANGLE FAULT TT-2.O"
5802	DECLINE 15-14	35.7	38.7	MP9-MP12	RIGHT UP	0.021	0.10	FG PLANAR LAMINATED ASH TUFF
5801	DECLINE 15-14	35.7	38.7	MP9-MP12	RIGHT MID	0.011	0.09	LOW ANGLE FAULT/CONTACT, TT-2.0'
5800	DECLINE 15-14	35.7	38.7	MP9-MP12	RIGHT LOW	0.009	0.10	FG PLANAR LAMINATED ASH TUFF
5799	DECLINE 15-14	32.1	35.7	MP9-MP12	RIGHT UP	0.006	0.09	FINE- COARSE-GRAINED PLANAR LAMINATED ASH TUFF
5798	DECLINE 15-14	32.1	35.7	MP9-MP12	RIGHT MID	0.006	0.05	LOW ANGLE FAULT/CONTACT, TT-2.0'
5797	DECLINE 15-14	32.1	35.7	MP9-MP12	RIGHT LOW	0.007	0.08	FG PLANAR LAMINATED ASH TUFF
5796	DECLINE 15-14	28.7	32.1	MP9-MP12	RIGHT UP	0.043	1.55	FINE- COARSE-GRAINED PLANAR LAMINATED ASH TUFF
5795	DECLINE 15-14	28.7	32.1	MP9-MP12	RIGHT MID	1.045	3.37	LOW ANGLE FAULT/CONTACT, TT-2.0'
5794	DECLINE 15-14	28.7	32.1	MP9-MP12	RIGHT LOW	0.042	0.14	FG PLANAR LAMINATED ASH TUFF
5778	DECLINE 15-14	9.5	12.6	MP12-MP15	RIGHT UP	0.001	0.04	FLOW BANDED VOLC BX W/S&S GRADING UPWARDS INTO VOLC BX W/O S&S?.
5780	DECLINE 15-14	9.5	12.6	MP12-MP15	RIGHT MID	0.001	0.04	LOW ANGLE FAULT, TT = 0.5 - 1.0", GREEN CLAY GOUGE + PY+/- MARC +/- CACO3
5779	DECLINE 15-14	9.5	12.6	MP12-MP15	RIGHT LOW	0.001	0.04	FG PLANAR LAMINATED ASH TUFF
5775	DECLINE 15-14	5.6	9.5	MP12-MP15	RIGHT UP	0.001	0.03	FLOW BANDED VOLC BX W/S&S GRADING UPWARDS INTO VOLC BX W/O S&S?
5777	DECLINE 15-14	5.6	9.5	MP12-MP15	RIGHT MID	0.001	0.05	LOW ANGLE FAULT, TT = 0.5", GREEN CLAY GOUGE + PY+/- MARC +/- CACO3
5776	DECLINE 15-14	5.6	9.5	MP12-MP15	RIGHT LOW	0.001	0.02	FG PLANAR LAMINATED ASH TUFF
5772	DECLINE 15-14	0.3	5.6	MP12-MP15	RIGHT UP	0.002	0.05	FLOW BANDED VOLC BX W/S&S GRADING UPWARDS INTO VOLC BX W/O S&S?
5774	DECLINE 15-14	0.3	5.6	MP12-MP15	RIGHT MID	0.001	0.04	LOW ANGLE FAULT, TT = 0.5", GREEN CLAY GOUGE + PY+/- MARC +/- CACO3
5773	DECLINE 15-14	0.3	5.6	MP12-MP15	RIGHT LOW	0.001	0.03	FG PLANAR LAMINATED ASH TUFF
5756	DECLINE 15-14	5.0	10.0	MP12-MP15	LEFT UP	0.002	0.05	MOD FLOW BANDED VOLC BX (WELDED) CLASTS ARE S&S
5759	DECLINE 15-14	5.0	10.0	MP12-MP15	LEFT MID	0.003	0.09	LOW ANGLE FAULT, TT = 0.5", GREEN CLAY GOUGE + PY+/- MARC +/- CACO3
5757	DECLINE 15-14	5.0	10.0	MP12-MP15	LEFT LOW	0.016	0.07	PLANAR LAMINATED ASH TUFF
5754	DECLINE 15-14	0.0	5.0	MP12-MP15	LEFT UP	0.003	0.04	HET, MS, VOLC BX (WELDED), CLASTS ARE SQUASHED AND STRETCHED.
5758	DECLINE 15-14	0.0	5.0	MP12-MP15	LEFT MID	0.005	0.09	LOW ANGLE FAULT, TT = 0.5", GREEN CLAY GOUGE + PY+/- MARC +/- CACO3
5755	DECLINE 15-14	0.0	5.0	MP12-MP15	LEFT LOW	0.005	0.07	PLANAR LAMINATED ASH TUFF BELOW LOW ANGLE FAULT
5771	DECLINE 14-13	37.6	38.7	MP12-MP15	LEFT	0.001	0.06	CACO3 +/- PY +/- CPY FRACTURE, TT=0.25-0.5"

SAMPLE #	LOCATION	FROM	TO	MAP POINTS	RIB	GOLD OPT	SILVER OPT	SAMPLE DESCRIPTION
5770	DECLINE 14-13	34.0	37.6	MP12-MP15	LEFT	0.001	0.05	MINOR FLOW BANDED VOLC BX (WELDED) CLASTS ARE MINOR S&S
5769	DECLINE 14-13	30.0	34.0	MP12-MP15	LEFT	0.002	0.08	MINOR FLOW BANDED VOLC BX (WELDED) CLASTS ARE MINOR S&S
5731	DECLINE @ 17	7.9	11.2	MP0-MP9	LEFT	0.003	0.04	HET, MS, VOLC BX.
5730	DECLINE @ 17	3.9	7.9	MP0-MP9	LEFT	0.003	0.07	HET, MS, VOLC BX.
5729	DECLINE @ 17	0.0	3.9	MP0-MP9	LEFT	0.025	0.15	HET, MS, VOLC BX.
5743	DECLINE @ 16	58.3	58.8	MP0-MP9	LEFT	0.062	0.13	MOD STRONG CACO3 + MARC +/-CPY FRACTURE, TT = 1".
5742	DECLINE @ 16	54.4	58.3	MP0-MP9	LEFT	0.001	0.04	HET, MS, VOLC BX, TT=1.3'.
5741	DECLINE @ 16	51.1	54.4	MP0-MP9	LEFT	0.004	0.02	HET, MS, VOLC BX.
5740	DECLINE @ 16	46.9	51.1	MP0-MP9	LEFT	0.002	0.04	F-G TO C-G MASSIVE ASH TUFF
5739	DECLINE @ 16	42.6	46.9	MP0-MP9	LEFT	0.001	0.02	F-G TO C-G MASSIVE ASH TUFF
5811	DECLINE @ 15	23.7	28.6	MP9-MP12	LEFT LOW	0.004	0.07	HET? VOLC BX W/STRONG S&S
5812	DECLINE @ 15	23.7	28.6	MP9-MP12	LEFT UP	0.003	0.05	HET? VOLC BX W/STRONG S&S
5768	DECLINE @ 14	28.0	30.0	MP12-MP15	LEFT	0.001	0.04	COARSELY PLANAR LAMINATED FG ASH TUFF
5767	DECLINE @ 14	25.0	28.0	MP12-MP15	LEFT	0.001	0.04	MINOR FLOW BANDED VOLC BX (WELDED) CLASTS ARE MINOR S&S
5766	DECLINE @ 14	20.0	25.0	MP12-MP15	LEFT	0.004	0.05	MINOR FLOW BANDED VOLC BX (WELDED) CLASTS ARE MINOR S&S
5762	DECLINE @ 14	15.0	20.0	MP12-MP15	LEFT UP	0.001	0.05	MINOR FLOW BANDED VOLC BX (WELDED) CLASTS ARE MINOR S&S
5763	DECLINE @ 14	15.0	20.0	MP12-MP15	LEFT LOW	0.002	0.05	PLANAR LAMINATED ASH TUFF
5765	DECLINE @ 14	15.0	20.0	MP12-MP15	LEFT MID	0.001	0.04	LOW ANGLE FAULT, TT = 0.5", GREEN CLAY GOUGE + PY+/- MARC +/- CACO3
5760	DECLINE @ 14	10.0	15.0	MP12-MP15	LEFT UP	0.001	0.05	FLOW BANDED VOLC BX (WELDED) CLASTS ARE S&S
5761	DECLINE @ 14	10.0	15.0	MP12-MP15	LEFT LOW	0.001	0.03	PLANAR LAMINATED ASH TUFF
5764	DECLINE @ 14	10.0	15.0	MP12-MP15	LEFT MID	0.001	0.05	LOW ANGLE FAULT, TT = 0.5", GREEN CLAY GOUGE + PY+/- MARC +/- CACO3
5647	DDS #16	MP11-4ROMP11	4ROMP-11	MP10-MP11	R FACE	0.051	0.2	HET, MS, VOLC BX, W/ MINOR LAMINATIONS.
5648	DDS #16	27.4	29.9	MP10-MP11	R FACE	2.450	6.89	F-G TO C-G MASSIVE ASH TUFF
5655	DDS #16	27.4	29.9	MP10-MP11	R FACE	0.066	0.26	FRACTURE WITH BLACK MUD-CEMENT "ONLY" (SAME SITE AS 5646)
5656	DDS #16	27.4	29.9	MP10-MP11	R FACE	47.200	20.10	SAME FRACTURE AS 5655 W/ WHITE CLAY + SULFIDES AND NO CEMENT
5649	DDS #16	25.1	27.4	MP10-MP11	R F-RIB	5.982	10.3	HET, MS, VOLC BX
5650	DDS #16	21.8	25.1	MP10-MP11	RIGHT	0.050	0.13	HET, MS, VOLC BX
5651	DDS #16	18.6	21.8	MP10-MP11	RIGHT	0.026	0.09	HET, MS, VOLC BX
5652	DDS #16	14.3	18.6	MP10-MP11	RIGHT	0.036	0.12	HET, MS, VOLC BX
5646	DDS #16	3LOMP11-MP11	MP-11	MP10-MP11	LEFT FACE	0.224	0.91	HET, MS, VOLC BX
5645	DDS #16	29.6-(3LOMP-11)	3LOMP-11	MP10-MP11	LEFT FACE	0.026	0.17	HET, MS, VOLC BX, ARGILLIZED
5644	DDS #16	27.6	29.6	MP10-MP11	LEFT R-F	0.019	0.13	HET, MS, VOLC BX
5643	DDS #16	24.1	27.6	MP10-MP11	LEFT	0.036	0.18	HET, MS, VOLC BX
5642	DDS #16	20.5	24.1	MP10-MP11	LEFT	0.049	0.25	HET, MS, VOLC BX
5641	DDS #16	18.5	20.5	MP10-MP11	LEFT	0.323	0.53	HET, MS, VOLC BX, W/ MOD COMMON CACO3 + MARC + CPY
5653	DDS #16	18.5	20.5	MP10-MP11	LEFT	1.270	1.03	CACO3 + SULFIDE VEINLETS "ONLY" (SAME SITE AS 5641)
5654	DDS #16	18.5	20.5	MP10-MP11	LEFT	0.030	0.07	ROCK "ONLY" W/ NO VEINLETS (SAME SITE AS 5641)
5788	DDS #15	MP14	3.4RO14	MP13-MP14	RIGHT F	0.014	0.10	FG PLANAR LAMINATED ASH TUFF
5789	DDS #15	3.4RO14	33.4	MP13-MP14	RIGHT F	0.008	0.15	FG PLANAR LAMINATED ASH TUFF
5790	DDS #15	29.4	33.4	MP13-MP14	RIGHT	0.011	0.10	FG PLANAR LAMINATED ASH TUFF
5791	DDS #15	25.0	29.4	MP13-MP14	RIGHT	0.009	0.18	FG PLANAR LAMINATED ASH TUFF
5792	DDS #15	20.2	25.0	MP13-MP14	RIGHT	0.009	0.26	FG PLANAR LAMINATED ASH TUFF
5793	DDS #15	16.0	20.2	MP13-MP14	RIGHT	0.016	0.15	FG PLANAR LAMINATED ASH TUFF
5786	DDS #15	30.7	34.3	MP13-MP14	LEFT R-F	0.047	0.18	FG PLANAR LAMINATED ASH TUFF
5787	DDS #15	34.3	MP14	MP13-MP14	LEFT F	0.030	0.17	FG PLANAR LAMINATED ASH TUFF
5785	DDS #15	27.6	30.7	MP13-MP14	LEFT	0.042	0.21	FG PLANAR LAMINATED ASH TUFF
5784	DDS #15	27.4	27.6	MP13-MP14	LEFT	1.380	2.40	FAULT
5783	DDS #15	24.1	27.4	MP13-MP14	LEFT	0.079	2.16	HET? VOLC BX W/S&S, MINOR DENSITY OF CACO3 + SULFIDE FRACTURES.
5782	DDS #15	21.4	24.1	MP13-MP14	LEFT	0.032	0.48	HET? VOLC BX W/S&S, MOD DENSITY OF CACO3 + SULFIDE FRACTURES.
5781	DDS #15	18.4	21.4	MP13-MP14	LEFT	0.438	0.69	HET? VOLC BX W/S&S, HIGH DENSITY OF CACO3 + SULFIDE FRACTURES.

AMERICAN ASSAY LABORATORIES

PROVISIONAL REPORT SP037954

CLIENT : HECLA MINING CO.
PROJECT : ROSEBUD
REFERENCE : 5747/5946

REPORTED : 26 APR 1996

SAMPLES	AU(OZ)	AU(RZ)	AUCRAV	AG(OZ)
5747	0.004			0.03
5748	0.004			0.13
5749	0.002			0.02
5750	0.003			0.02
5751	0.006			0.07
5752	1.138			1.69
5820	0.001			0.02
5821	0.006			0.02
5822	0.003			0.02
5823	0.183	0.209		0.28
5824	0.069			0.11
5825	0.002			<0.02
5826	0.006			0.02
5827	0.194			0.28
5828	0.002			0.02
5829	0.002			0.05
5830	0.008			0.04
5857	0.004			0.06
5858	0.002			0.07
5859	0.002			<0.02
5860	<0.001			0.03
5861	0.001			0.02
5862	0.003			0.03
5863	0.002			0.02
5864	0.016			0.06

AMERICAN ASSAY LABORATORIES

PROVISIONAL REPORT SP037954

CLIENT : HECLA MINING CO.
PROJECT : ROSEBUD
REFERENCE : 5747/5946

REPORTED : 26 APR 1996

SAMPLES	Au(OZ)	Au(RZ)	AuCRAV	Ag(OZ)
5865	0.015			0.07
5866	0.004			0.05
5867	0.001			0.02
5868	0.001			0.02
5869	0.002			0.03
5870	0.002			0.04
5871	<0.001			0.02
5872	<0.001			0.02
5874	<0.001			0.02
5875	<0.001			0.02
5876	0.003			0.04
5877	0.001			0.05
5878	<0.001			<0.02
5879	<0.001			<0.02
5880	<0.001			<0.02
5881	0.003	0.004		0.05
5882	<0.001			<0.02
5883	0.002			0.03
5884	0.003			0.03
5887	<0.001			<0.02
5888	<0.001			<0.02
5889	0.002			0.02
5890	<0.001			<0.02
5891	<0.001			<0.02
5892	0.001			<0.02

AMERICAN ASSAY LABORATORIES

PROVISIONAL REPORT SP037954

CLIENT : HECLA MINING CO.
PROJECT : ROSEBUD
REFERENCE : 5747/5946

REPORTED : 26 APR 1996

SAMPLES	AU(OZ)	AU(RZ)	AU(GRAV)	AG(OZ)
5893	0.001			<0.02
5894	0.003			0.02
5895	<0.001			0.02
5896	<0.001			<0.02
5897	0.001			0.03
5898	<0.001			<0.02
5899	<0.001			<0.02
5900	0.001			<0.02
5901	0.066	0.060		0.10
5902	<0.001			<0.02
5926	<0.001			<0.02
5927	0.001			<0.02
5928	<0.001			<0.02
5929	<0.001			0.02
5930	<0.001			<0.02
5931	<0.001			<0.02
5932	0.001			0.02
5946	0.003			0.03

SURVEY

~~D-99-95 - 18½~~

D-104-95 - 16½ CALLED OFF

D-105-95 - 16½ ✓

D-108-95 - 16½ ✓

D-112-95 - 15½

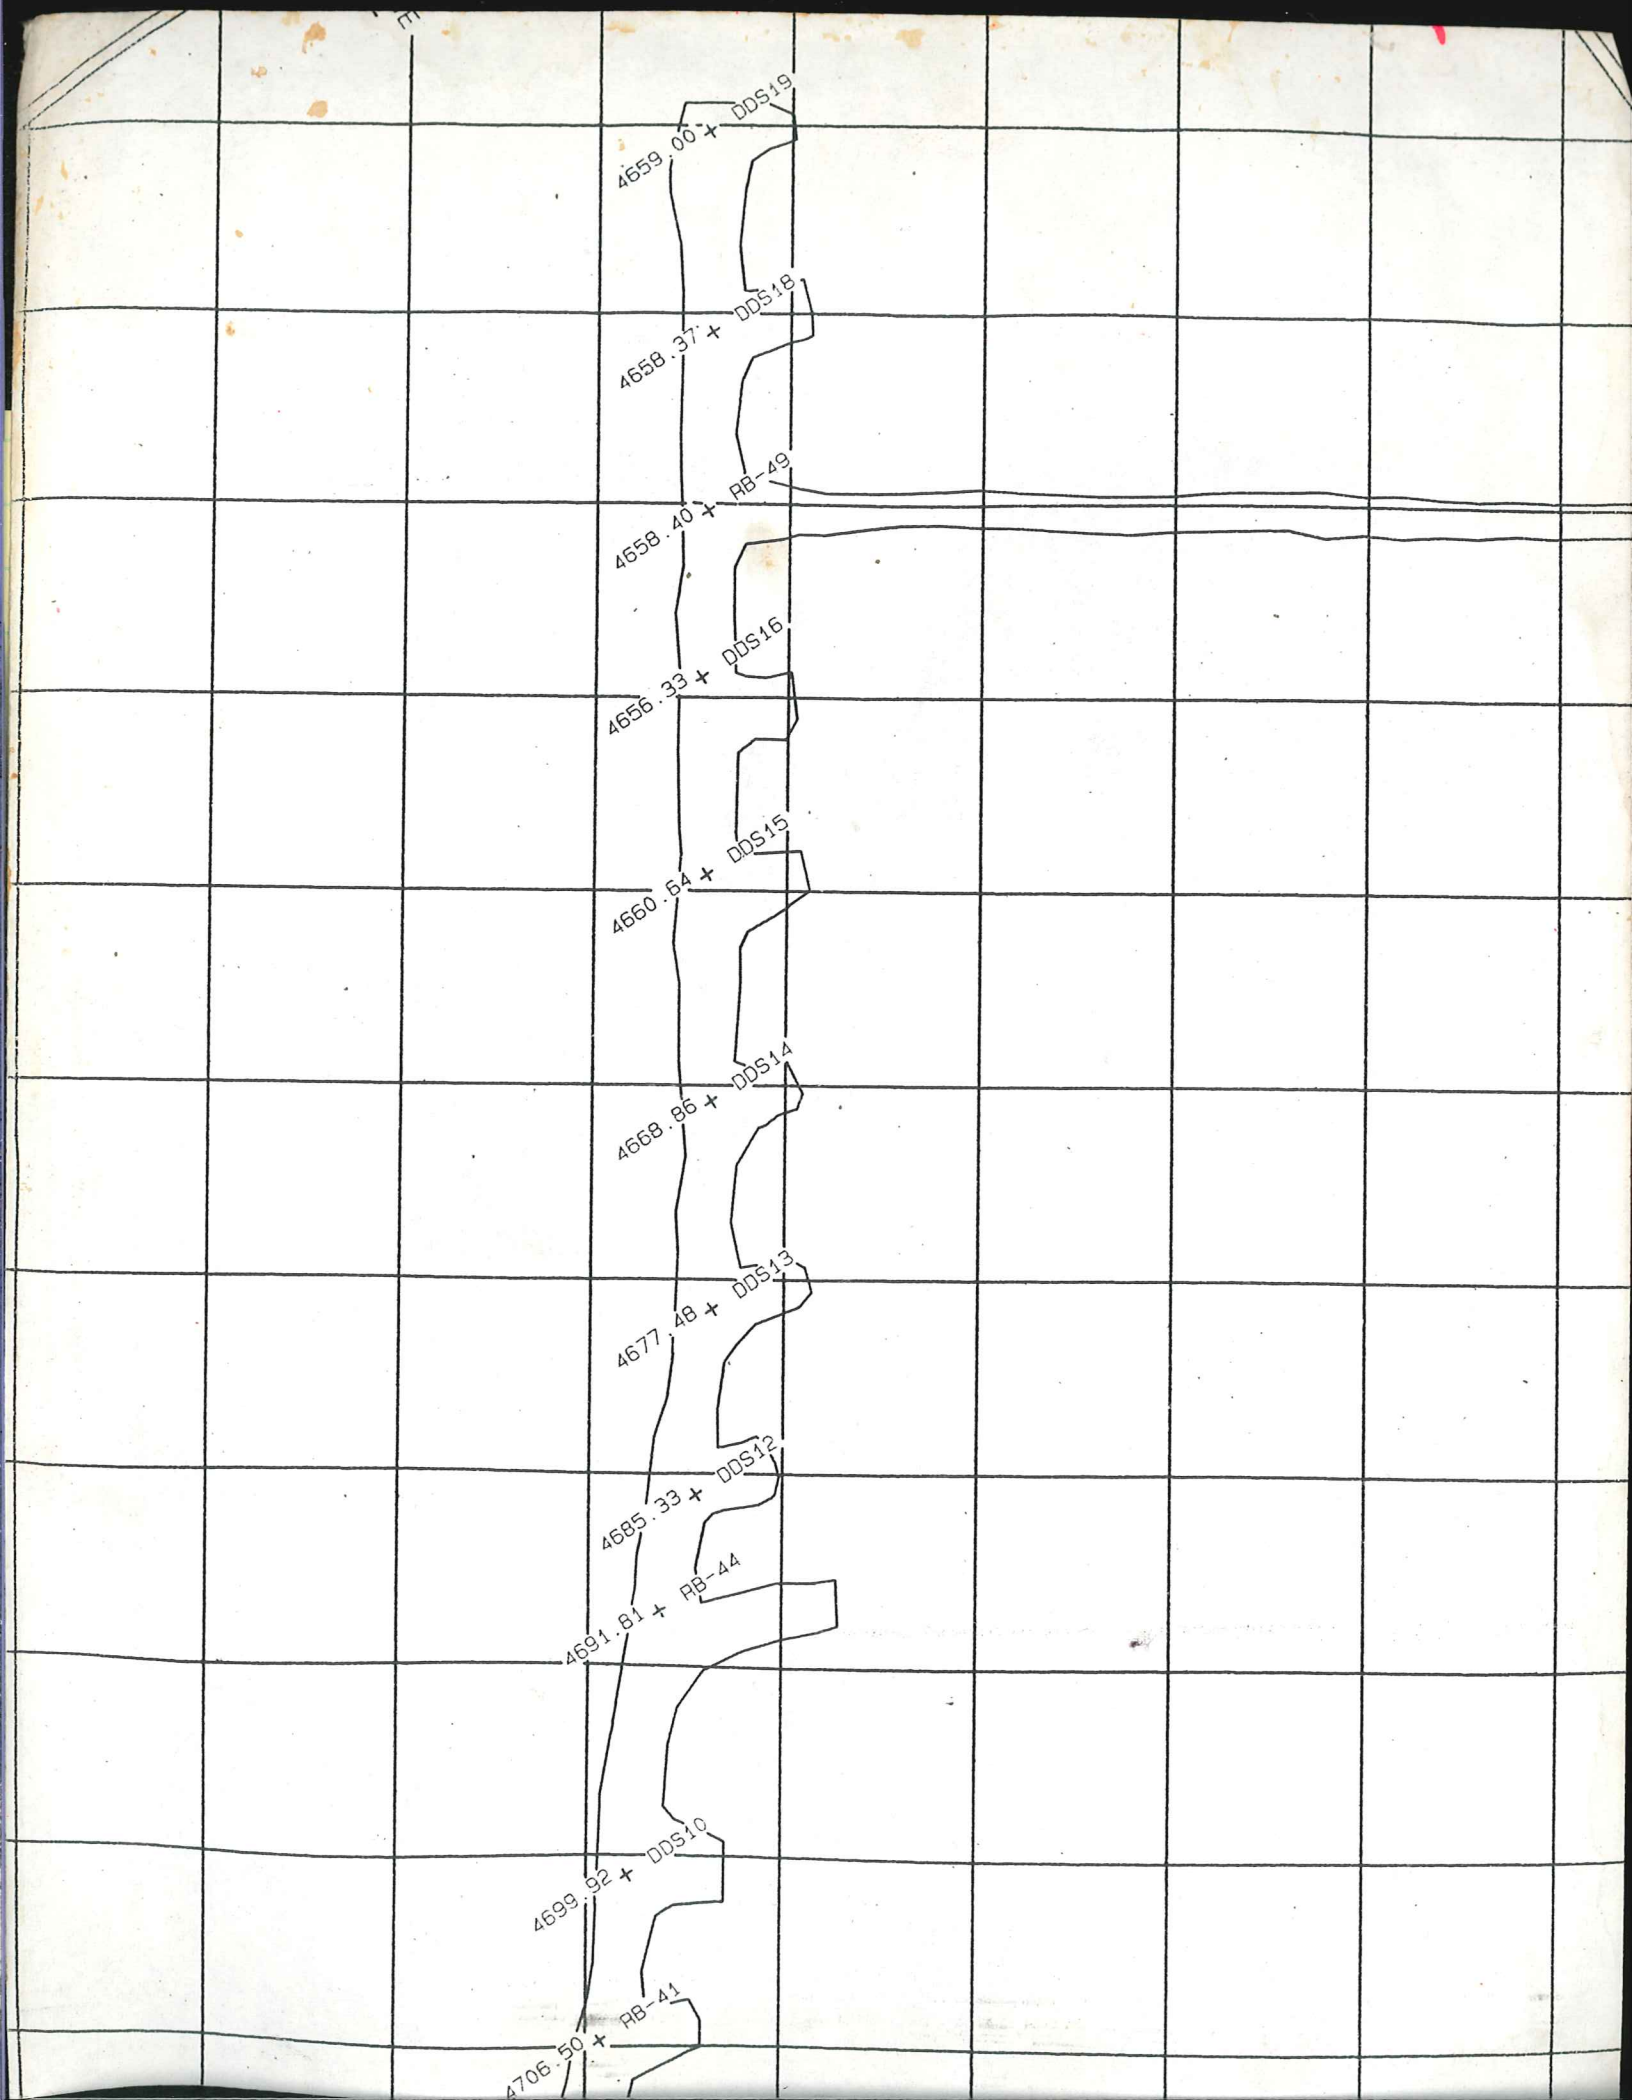
DDS19
4659.00
DDS18
4658.37
RB-49
4658.40
DDS16
4656.33
DDS15
4660.64
DDS14
4668.86
DDS13
4677.48
DDS12
4685.33
RB-44
4691.81
DDS10
4699.92
RB-41
4706.50
